

Work Order ID 93738

93738

Page 1

November-27-12 10:47:43 AM

Item ID: D350-748-201

Accept

N900040100

Setup Start *NS1*

Revision ID:

Stop *NS2*

Item Name: Crosstube Installation, High Aft

Start Date: 11/22/12 Start Qty: 1.00

1

Cust Item ID:

Required Date: 12/21/12 Req'd Qty: 1.00

1

Customer:

Reference:

Run Start *NR1*

Approvals: Process Plan: ML5 Date: 12-11-23 Tooling: _____ Date: _____

Stop *NR2*

QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

| Sequence ID/ Work Center ID | Operation Description | Set Up/ Run Hours | Tool ID | Tool # | Plan Code | Accept Qty | Reject Qty | Reject Number | Insp. Stamp |
|--------------------------------|--------------------------|----------------------|---------|--------|--------------|---------------|---------------|------------------|----------------|
|--------------------------------|--------------------------|----------------------|---------|--------|--------------|---------------|---------------|------------------|----------------|

Draw Nbr

Revision Nbr

D350-748-241

100

0.00

100

DC

Document Control

DOCUMENT CONTROL

Memo

Photocopy bluefile & type labels per PPPD350-748-201

0.00

CHG003

110

0.00

110

CNC Bend 2

CNC Alpha 160 Bender

BENDING MACHINE - CROSSTUBES

Memo

Bend tube as per Dwg D350-748-241 using CNC bender program D350A and Folio FT

****UNDER BEND .225" PER SIDE****

****USE (4) DT9824 SHIM BLOC TO CHECK STRAIGHTNESS****

DAG
16

12/12/12

UP 12/12/12

CHG 002

12-12-3

NOV 13

NCR: Yes / No

WORK ORDER NON-CONFORMANCE / UPDATE

DQA: _____ Date: _____

QA Closed: _____ Date: _____

| | | | | | | | | | | | | | | | | | | |
|--|---|---|--------------------------------------|------------------------------------|------------------------------------|--------------------------------------|------------------------------------|------------------------------------|--|----------------------------------|--|------------------------------------|--|--------------------------------|------------------------------------|------------------------------------|-----------------------------------|--|
| Work Order: _____ Part No. _____ NCR No. _____ | DISPOSITION Rework <input type="checkbox"/> Scrap <input type="checkbox"/> Use-as-is <input type="checkbox"/> Work Order Update <input type="checkbox"/> | AGAINST DEPARTMENT/PROCESS <table style="width: 100%;"> <tr> <td>Skid-tube <input type="checkbox"/></td> <td>Crosstube <input type="checkbox"/></td> <td>Water Jet <input type="checkbox"/></td> <td>Engineering <input type="checkbox"/></td> </tr> <tr> <td>Machining <input type="checkbox"/></td> <td>Small Fab <input type="checkbox"/></td> <td>Prod. Eng. Coord. <input type="checkbox"/></td> <td>Quality <input type="checkbox"/></td> </tr> <tr> <td>Thermoforming <input type="checkbox"/></td> <td>Finishing <input type="checkbox"/></td> <td>Rec/Store/Packaging <input type="checkbox"/></td> <td>Other <input type="checkbox"/></td> </tr> <tr> <td>Large Fab <input type="checkbox"/></td> <td>Composite <input type="checkbox"/></td> <td>Supplier <input type="checkbox"/></td> <td></td> </tr> </table> | Skid-tube <input type="checkbox"/> | Crosstube <input type="checkbox"/> | Water Jet <input type="checkbox"/> | Engineering <input type="checkbox"/> | Machining <input type="checkbox"/> | Small Fab <input type="checkbox"/> | Prod. Eng. Coord. <input type="checkbox"/> | Quality <input type="checkbox"/> | Thermoforming <input type="checkbox"/> | Finishing <input type="checkbox"/> | Rec/Store/Packaging <input type="checkbox"/> | Other <input type="checkbox"/> | Large Fab <input type="checkbox"/> | Composite <input type="checkbox"/> | Supplier <input type="checkbox"/> | |
| Skid-tube <input type="checkbox"/> | Crosstube <input type="checkbox"/> | Water Jet <input type="checkbox"/> | Engineering <input type="checkbox"/> | | | | | | | | | | | | | | | |
| Machining <input type="checkbox"/> | Small Fab <input type="checkbox"/> | Prod. Eng. Coord. <input type="checkbox"/> | Quality <input type="checkbox"/> | | | | | | | | | | | | | | | |
| Thermoforming <input type="checkbox"/> | Finishing <input type="checkbox"/> | Rec/Store/Packaging <input type="checkbox"/> | Other <input type="checkbox"/> | | | | | | | | | | | | | | | |
| Large Fab <input type="checkbox"/> | Composite <input type="checkbox"/> | Supplier <input type="checkbox"/> | | | | | | | | | | | | | | | | |

| Root Cause | Date | Step | Qty | Description of work order update or Non-conformance | Initial Chief Eng | Action Description | Sign & Date | Verification | QC Inspector |
|---------------|------|------|-----|---|-------------------|--------------------|-------------|--------------|--------------|
| Doc/Data | | | | | | | | | |
| Equip/Tooling | | | | | | | | | |
| Operator | | | | | | | | | |
| Material | | | | | | | | | |
| Setup | | | | | | | | | |
| Other | | | | | | | | | |
| Process | | | | | | | | | |
| Supplier | | | | | | | | | |
| Training | | | | | | | | | |
| Unapproved | | | | | | | | | |

FAULT CATEGORY

| Landing Gear | General | Other |
|---|---|--|
| <input type="checkbox"/> Bending | <input type="checkbox"/> Bend | <input type="checkbox"/> Grain |
| <input type="checkbox"/> Centre Not Concentric to O/S | <input type="checkbox"/> BOM/Route | <input type="checkbox"/> Hardware |
| <input type="checkbox"/> Cracks | <input type="checkbox"/> Broken/Damaged | <input type="checkbox"/> Inspection Incomplete |
| <input type="checkbox"/> Crushed/Crimped | <input type="checkbox"/> Burrs | <input type="checkbox"/> Instructions Incomplete/Unclear |
| <input type="checkbox"/> Cuffs | <input type="checkbox"/> Contamination | <input type="checkbox"/> Maintenance |
| <input type="checkbox"/> Heat Treat | <input type="checkbox"/> Countersink | <input type="checkbox"/> Mislabeled |
| <input type="checkbox"/> Inspection Strip in Tube | <input type="checkbox"/> Cut Too Short | <input type="checkbox"/> Misread |
| <input type="checkbox"/> Ripples in Bend | <input type="checkbox"/> Drill Holes | <input type="checkbox"/> Offset |
| <input type="checkbox"/> Torque Waves in Extrusion | <input type="checkbox"/> Drawing | <input type="checkbox"/> Out of Calibration |
| <input type="checkbox"/> Turning Sequence | <input type="checkbox"/> Finish | <input type="checkbox"/> Out of Sequence |
| <input type="checkbox"/> Wave/Twist in Tube | <input type="checkbox"/> Folio | <input type="checkbox"/> Outside Dimensions |
| | | <input type="checkbox"/> Ovalized |
| | | <input type="checkbox"/> Over/Under tolerance |
| | | <input type="checkbox"/> Part Incorrect |
| | | <input type="checkbox"/> Part Lost/Missing |
| | | <input type="checkbox"/> Part Moved |
| | | <input type="checkbox"/> Positioned Wrong |
| | | <input type="checkbox"/> Power Loss/Surge |
| | | <input type="checkbox"/> Pressure/Forced |
| | | <input type="checkbox"/> Temperature/Cure |
| | | <input type="checkbox"/> Weld |
| | | <input type="checkbox"/> Wrong Stock Pulled |
| | | <input type="checkbox"/> Other |

Work Order ID 93738

93738

Page 2

November-27-12 10:47:43 AM

Item ID: D350-748-201

Accept

N900040100

Setup Start *NS1*

Revision ID:

Stop *NS2*

Item Name: Crosstube Installation, High Aft

Start Date: 11/22/12 Start Qty: 1.00 *1*

Cust Item ID:

Required Date: 12/21/12 Req'd Qty: 1.00 *1*

Customer:

Reference:

Approvals: Process Plan: Date: Tooling: Date:

Run Start *NR1*

QC: Date: SPC (Y/N): Date:

Stop *NR2*

| Sequence ID/ Work Center ID | Operation Description | Set Up/ Run Hours | Tool ID | Tool # | Plan Code | Accept Qty | Reject Qty | Reject Number | Insp. Stamp |
|---|--|----------------------|---------|--------|--------------|---------------|---------------|------------------|----------------|
| 120 *120* QC Quality Control | QC15- Crosstube Dimensional Check as Memo ***USE (4) DT9824 SHIM BLOC TO CHECK STRAIGHTNESS*** | 0.00 0.00 | | | | | | | |
| 125 *125* HandFXtube Hand Finishing Crosstubes | HandFXtube Hand Finishing Crosstubes Memo ***Stress relief*** Heat treat crosstube as per QSI010 4.3 Temp: _____ Start time: _____ Finish time: _____ | 0.00 0.00 | | | | | | | |
| 127 *127* QC Quality Control | QC15- Crosstube Dimensional Check Memo | 0.00 0.00 | | | | | | | |

see'd
see'd + inspect
attached c/c to w/o

12/1/12


NCR: Yes / No

WORK ORDER NON-CONFORMANCE / UPDATE

DQA: _____ Date: _____

QA Closed: _____ Date: _____

| | | | | | | | | | | | | | | | | | | |
|--|--|--|--------------------------------------|------------------------------------|------------------------------------|--------------------------------------|------------------------------------|------------------------------------|--|----------------------------------|--|------------------------------------|--|--------------------------------|------------------------------------|------------------------------------|-----------------------------------|--|
| Work Order: _____ Part No. _____ NCR No. _____ | DISPOSITION Rework <input type="checkbox"/> Scrap <input type="checkbox"/> Use-as-is <input type="checkbox"/> Work Order Update <input checked="" type="checkbox"/> | AGAINST DEPARTMENT/PROCESS <table style="width:100%;"> <tr> <td>Skid-tube <input type="checkbox"/></td> <td>Crosstube <input type="checkbox"/></td> <td>Water Jet <input type="checkbox"/></td> <td>Engineering <input type="checkbox"/></td> </tr> <tr> <td>Machining <input type="checkbox"/></td> <td>Small Fab <input type="checkbox"/></td> <td>Prod. Eng. Coord. <input type="checkbox"/></td> <td>Quality <input type="checkbox"/></td> </tr> <tr> <td>Thermoforming <input type="checkbox"/></td> <td>Finishing <input type="checkbox"/></td> <td>Rec/Store/Packaging <input type="checkbox"/></td> <td>Other <input type="checkbox"/></td> </tr> <tr> <td>Large Fab <input type="checkbox"/></td> <td>Composite <input type="checkbox"/></td> <td>Supplier <input type="checkbox"/></td> <td></td> </tr> </table> | Skid-tube <input type="checkbox"/> | Crosstube <input type="checkbox"/> | Water Jet <input type="checkbox"/> | Engineering <input type="checkbox"/> | Machining <input type="checkbox"/> | Small Fab <input type="checkbox"/> | Prod. Eng. Coord. <input type="checkbox"/> | Quality <input type="checkbox"/> | Thermoforming <input type="checkbox"/> | Finishing <input type="checkbox"/> | Rec/Store/Packaging <input type="checkbox"/> | Other <input type="checkbox"/> | Large Fab <input type="checkbox"/> | Composite <input type="checkbox"/> | Supplier <input type="checkbox"/> | |
| Skid-tube <input type="checkbox"/> | Crosstube <input type="checkbox"/> | Water Jet <input type="checkbox"/> | Engineering <input type="checkbox"/> | | | | | | | | | | | | | | | |
| Machining <input type="checkbox"/> | Small Fab <input type="checkbox"/> | Prod. Eng. Coord. <input type="checkbox"/> | Quality <input type="checkbox"/> | | | | | | | | | | | | | | | |
| Thermoforming <input type="checkbox"/> | Finishing <input type="checkbox"/> | Rec/Store/Packaging <input type="checkbox"/> | Other <input type="checkbox"/> | | | | | | | | | | | | | | | |
| Large Fab <input type="checkbox"/> | Composite <input type="checkbox"/> | Supplier <input type="checkbox"/> | | | | | | | | | | | | | | | | |

| Root Cause | Date | Step | Qty | Description of work order update or Non-conformance | Initial Chief Eng | Action Description | Sign & Date | Verification | QC Inspector |
|--|------|------|-----|---|-------------------|--------------------|-------------|--------------|--|
| Doc/Data <input type="checkbox"/> | | | | change step # 120 to QLS Perm. Instr. | | | | |  11/2/07 |
| Equip/Tooling <input type="checkbox"/> | | | | | | | | | |
| Operator <input type="checkbox"/> | | | | | | | | | |
| Material <input type="checkbox"/> | | | | | | | | | |
| Setup <input type="checkbox"/> | | | | | | | | | |
| Other <input type="checkbox"/> | | | | | | | | | |
| Process <input type="checkbox"/> | | | | | | | | | |
| Supplier <input type="checkbox"/> | | | | | | | | | |
| Training <input type="checkbox"/> | | | | | | | | | |
| Unapproved <input type="checkbox"/> | | | | | | | | | |

FAULT CATEGORY

| Landing Gear | General | Other |
|---|---|--|
| <input type="checkbox"/> Bending | <input type="checkbox"/> Bend | <input type="checkbox"/> Grain |
| <input type="checkbox"/> Centre Not Concentric to O/S | <input type="checkbox"/> BOM/Route | <input type="checkbox"/> Hardware |
| <input type="checkbox"/> Cracks | <input type="checkbox"/> Broken/Damaged | <input type="checkbox"/> Inspection Incomplete |
| <input type="checkbox"/> Crushed/Crimped | <input type="checkbox"/> Burrs | <input type="checkbox"/> Instructions Incomplete/Unclear |
| <input type="checkbox"/> Cuffs | <input type="checkbox"/> Contamination | <input type="checkbox"/> Maintenance |
| <input type="checkbox"/> Heat Treat | <input type="checkbox"/> Countersink | <input type="checkbox"/> Mislabeled |
| <input type="checkbox"/> Inspection Strip in Tube | <input type="checkbox"/> Cut Too Short | <input type="checkbox"/> Misread |
| <input type="checkbox"/> Ripples in Bend | <input type="checkbox"/> Drill Holes | <input type="checkbox"/> Offset |
| <input type="checkbox"/> Torque Waves in Extrusion | <input type="checkbox"/> Drawing | <input type="checkbox"/> Out of Calibration |
| <input type="checkbox"/> Turning Sequence | <input type="checkbox"/> Finish | <input type="checkbox"/> Out of Sequence |
| <input type="checkbox"/> Wave/Twist in Tube | <input type="checkbox"/> Folio | <input type="checkbox"/> Outside Dimensions |
| | | <input type="checkbox"/> Ovalized |
| | | <input type="checkbox"/> Over/Under tolerance |
| | | <input type="checkbox"/> Part Incorrect |
| | | <input type="checkbox"/> Part Lost/Missing |
| | | <input type="checkbox"/> Part Moved |
| | | <input type="checkbox"/> Positioned Wrong |
| | | <input type="checkbox"/> Power Loss/Surge |
| | | <input type="checkbox"/> Pressure/Forced |
| | | <input type="checkbox"/> Temperature/Cure |
| | | <input type="checkbox"/> Weld |
| | | <input type="checkbox"/> Wrong Stock Pulled |
| | | <input type="checkbox"/> Other |

Work Order ID 93738

93738

Page 3

November-27-12 10:47:43 AM

Item ID: D350-748-201 Accept *N900040100* Setup Start *NS1*
 Revision ID: Stop *NS2*
 Item Name: Crosstube Installation, High Aft
 Start Date: 11/22/12 Start Qty: 1.00 *1* Cust Item ID:
 Required Date: 12/21/12 Req'd Qty: 1.00 *1* Customer:
 Reference:

Approvals: Process Plan: Date: Tooling: Date: Run Start *NR1*
 QC: Date: SPC (Y/N): Date: Stop *NR2*

| Sequence ID/ Work Center ID | Operation Description | Set Up/ Run Hours | Tool ID | Tool # | Plan Code | Accept Qty | Reject Qty | Reject Number | Insp. Stamp |
|--------------------------------|--|----------------------|---------|--------|--------------|---------------|---------------|------------------|----------------|
| 130 | Crosstubes | 0.00 | | | | | | | |
| *130* | | | | | | | | | |
| Crosstubes | Memo | 0.00 | | | | | | | |
| Crosstubes | 1-Drill Tube as per Dwg D350-748-241 Using DT8876 Drill Jigs, Set-up drill table as per QSI 010 | | | | | | | | |
| | 2-Deburr | | | | | | | | |
| | 3-Engrave Part # and Batch # as per Dwg D350-748-241 | | | | | | | | |
| | 4-Remove all marks from tube within limits of D350-748-241 | | | | | | | | |
| | 5- Apply a light coat of LPS3 on the interior of tube Batch: <u>WLAS</u> | | | | | | | | |
| 140 | QC6- Inspect dimensions to drawing | 0.00 | | | | | | | |
| *140* | | | | | | | | | |
| QC | Memo | 0.00 | | | | | | | |
| Quality Control | | | | | | | | | |

JW 12-12-6
 MO 12/12/06
 DAS 16
 12/12/07

NCR: Yes / No

WORK ORDER NON-CONFORMANCE / UPDATE

DQA: _____ Date: _____

QA Closed: _____ Date: _____

| | | | | | | | | | | | | | | | | | | |
|--|---|---|--------------------------------------|------------------------------------|------------------------------------|--------------------------------------|------------------------------------|------------------------------------|--|----------------------------------|--|------------------------------------|--|--------------------------------|------------------------------------|------------------------------------|-----------------------------------|--|
| Work Order: _____ Part No. _____ NCR No. _____ | DISPOSITION Rework <input type="checkbox"/> Scrap <input type="checkbox"/> Use-as-is <input type="checkbox"/> Work Order Update <input type="checkbox"/> | AGAINST DEPARTMENT/PROCESS <table style="width: 100%;"> <tr> <td>Skid-tube <input type="checkbox"/></td> <td>Crosstube <input type="checkbox"/></td> <td>Water Jet <input type="checkbox"/></td> <td>Engineering <input type="checkbox"/></td> </tr> <tr> <td>Machining <input type="checkbox"/></td> <td>Small Fab <input type="checkbox"/></td> <td>Prod. Eng. Coord. <input type="checkbox"/></td> <td>Quality <input type="checkbox"/></td> </tr> <tr> <td>Thermoforming <input type="checkbox"/></td> <td>Finishing <input type="checkbox"/></td> <td>Rec/Store/Packaging <input type="checkbox"/></td> <td>Other <input type="checkbox"/></td> </tr> <tr> <td>Large Fab <input type="checkbox"/></td> <td>Composite <input type="checkbox"/></td> <td>Supplier <input type="checkbox"/></td> <td></td> </tr> </table> | Skid-tube <input type="checkbox"/> | Crosstube <input type="checkbox"/> | Water Jet <input type="checkbox"/> | Engineering <input type="checkbox"/> | Machining <input type="checkbox"/> | Small Fab <input type="checkbox"/> | Prod. Eng. Coord. <input type="checkbox"/> | Quality <input type="checkbox"/> | Thermoforming <input type="checkbox"/> | Finishing <input type="checkbox"/> | Rec/Store/Packaging <input type="checkbox"/> | Other <input type="checkbox"/> | Large Fab <input type="checkbox"/> | Composite <input type="checkbox"/> | Supplier <input type="checkbox"/> | |
| Skid-tube <input type="checkbox"/> | Crosstube <input type="checkbox"/> | Water Jet <input type="checkbox"/> | Engineering <input type="checkbox"/> | | | | | | | | | | | | | | | |
| Machining <input type="checkbox"/> | Small Fab <input type="checkbox"/> | Prod. Eng. Coord. <input type="checkbox"/> | Quality <input type="checkbox"/> | | | | | | | | | | | | | | | |
| Thermoforming <input type="checkbox"/> | Finishing <input type="checkbox"/> | Rec/Store/Packaging <input type="checkbox"/> | Other <input type="checkbox"/> | | | | | | | | | | | | | | | |
| Large Fab <input type="checkbox"/> | Composite <input type="checkbox"/> | Supplier <input type="checkbox"/> | | | | | | | | | | | | | | | | |

| Root Cause | Date | Step | Qty | Description of work order update or Non-conformance | Initial Chief Eng | Action Description | Sign & Date | Verification | QC Inspector |
|---------------|------|------|-----|---|-------------------|--------------------|-------------|--------------|--------------|
| Doc/Data | | | | | | | | | |
| Equip/Tooling | | | | | | | | | |
| Operator | | | | | | | | | |
| Material | | | | | | | | | |
| Setup | | | | | | | | | |
| Other | | | | | | | | | |
| Process | | | | | | | | | |
| Supplier | | | | | | | | | |
| Training | | | | | | | | | |
| Unapproved | | | | | | | | | |

FAULT CATEGORY

| Landing Gear | General | Other |
|---|---|--|
| <input type="checkbox"/> Bending | <input type="checkbox"/> Bend | <input type="checkbox"/> Grain |
| <input type="checkbox"/> Centre Not Concentric to O/S | <input type="checkbox"/> BOM/Route | <input type="checkbox"/> Hardware |
| <input type="checkbox"/> Cracks | <input type="checkbox"/> Broken/Damaged | <input type="checkbox"/> Inspection Incomplete |
| <input type="checkbox"/> Crushed/Crimped | <input type="checkbox"/> Burrs | <input type="checkbox"/> Instructions Incomplete/Unclear |
| <input type="checkbox"/> Cuffs | <input type="checkbox"/> Contamination | <input type="checkbox"/> Maintenance |
| <input type="checkbox"/> Heat Treat | <input type="checkbox"/> Countersink | <input type="checkbox"/> Mislabeled |
| <input type="checkbox"/> Inspection Strip in Tube | <input type="checkbox"/> Cut Too Short | <input type="checkbox"/> Misread |
| <input type="checkbox"/> Ripples in Bend | <input type="checkbox"/> Drill Holes | <input type="checkbox"/> Offset |
| <input type="checkbox"/> Torque Waves in Extrusion | <input type="checkbox"/> Drawing | <input type="checkbox"/> Out of Calibration |
| <input type="checkbox"/> Turning Sequence | <input type="checkbox"/> Finish | <input type="checkbox"/> Out of Sequence |
| <input type="checkbox"/> Wave/Twist in Tube | <input type="checkbox"/> Folio | <input type="checkbox"/> Outside Dimensions |
| | | <input type="checkbox"/> Ovalized |
| | | <input type="checkbox"/> Over/Under tolerance |
| | | <input type="checkbox"/> Part Incorrect |
| | | <input type="checkbox"/> Part Lost/Missing |
| | | <input type="checkbox"/> Part Moved |
| | | <input type="checkbox"/> Positioned Wrong |
| | | <input type="checkbox"/> Power Loss/Surge |
| | | <input type="checkbox"/> Pressure/Forced |
| | | <input type="checkbox"/> Temperature/Cure |
| | | <input type="checkbox"/> Weld |
| | | <input type="checkbox"/> Wrong Stock Pulled |
| | | <input type="checkbox"/> Other |

NCR: Yes / No

WORK ORDER NON-CONFORMANCE / UPDATE

DQA: _____ Date: _____

QA Closed: _____ Date: _____

| | | | | | | | | | | | | | | | | | | |
|--|---|---|--------------------------------------|------------------------------------|------------------------------------|--------------------------------------|------------------------------------|------------------------------------|--|----------------------------------|--|------------------------------------|--|--------------------------------|------------------------------------|------------------------------------|-----------------------------------|--|
| Work Order: _____ Part No. _____ NCR No. _____ | DISPOSITION Rework <input type="checkbox"/> Scrap <input type="checkbox"/> Use-as-is <input type="checkbox"/> Work Order Update <input type="checkbox"/> | AGAINST DEPARTMENT/PROCESS <table style="width: 100%;"> <tr> <td>Skid-tube <input type="checkbox"/></td> <td>Crosstube <input type="checkbox"/></td> <td>Water Jet <input type="checkbox"/></td> <td>Engineering <input type="checkbox"/></td> </tr> <tr> <td>Machining <input type="checkbox"/></td> <td>Small Fab <input type="checkbox"/></td> <td>Prod. Eng. Coord. <input type="checkbox"/></td> <td>Quality <input type="checkbox"/></td> </tr> <tr> <td>Thermoforming <input type="checkbox"/></td> <td>Finishing <input type="checkbox"/></td> <td>Rec/Store/Packaging <input type="checkbox"/></td> <td>Other <input type="checkbox"/></td> </tr> <tr> <td>Large Fab <input type="checkbox"/></td> <td>Composite <input type="checkbox"/></td> <td>Supplier <input type="checkbox"/></td> <td></td> </tr> </table> | Skid-tube <input type="checkbox"/> | Crosstube <input type="checkbox"/> | Water Jet <input type="checkbox"/> | Engineering <input type="checkbox"/> | Machining <input type="checkbox"/> | Small Fab <input type="checkbox"/> | Prod. Eng. Coord. <input type="checkbox"/> | Quality <input type="checkbox"/> | Thermoforming <input type="checkbox"/> | Finishing <input type="checkbox"/> | Rec/Store/Packaging <input type="checkbox"/> | Other <input type="checkbox"/> | Large Fab <input type="checkbox"/> | Composite <input type="checkbox"/> | Supplier <input type="checkbox"/> | |
| Skid-tube <input type="checkbox"/> | Crosstube <input type="checkbox"/> | Water Jet <input type="checkbox"/> | Engineering <input type="checkbox"/> | | | | | | | | | | | | | | | |
| Machining <input type="checkbox"/> | Small Fab <input type="checkbox"/> | Prod. Eng. Coord. <input type="checkbox"/> | Quality <input type="checkbox"/> | | | | | | | | | | | | | | | |
| Thermoforming <input type="checkbox"/> | Finishing <input type="checkbox"/> | Rec/Store/Packaging <input type="checkbox"/> | Other <input type="checkbox"/> | | | | | | | | | | | | | | | |
| Large Fab <input type="checkbox"/> | Composite <input type="checkbox"/> | Supplier <input type="checkbox"/> | | | | | | | | | | | | | | | | |

| Root Cause | Date | Step | Qty | Description of work order update or Non-conformance | Initial Chief Eng | Action Description | Sign & Date | Verification | QC Inspector |
|--|------|------|-----|---|-------------------|--------------------|-------------|--------------|--------------|
| Doc/Data <input type="checkbox"/> | | | | | | | | | |
| Equip/Tooling <input type="checkbox"/> | | | | | | | | | |
| Operator <input type="checkbox"/> | | | | | | | | | |
| Material <input type="checkbox"/> | | | | | | | | | |
| Setup <input type="checkbox"/> | | | | | | | | | |
| Other <input type="checkbox"/> | | | | | | | | | |
| Process <input type="checkbox"/> | | | | | | | | | |
| Supplier <input type="checkbox"/> | | | | | | | | | |
| Training <input type="checkbox"/> | | | | | | | | | |
| Unapproved <input type="checkbox"/> | | | | | | | | | |

FAULT CATEGORY

| | | |
|--|---|--|
| Landing Gear <input type="checkbox"/> Bending <input type="checkbox"/> Centre Not Concentric to O/S <input type="checkbox"/> Cracks <input type="checkbox"/> Crushed/Crimped. <input type="checkbox"/> Cuffs <input type="checkbox"/> Heat Treat <input type="checkbox"/> Inspection Strip in Tube <input type="checkbox"/> Ripples in Bend <input type="checkbox"/> Torque Waves in Extrusion <input type="checkbox"/> Turning Sequence <input type="checkbox"/> Wave/Twist in Tube | General <input type="checkbox"/> Bend <input type="checkbox"/> BOM/Route <input type="checkbox"/> Broken/Damaged <input type="checkbox"/> Burrs <input type="checkbox"/> Contamination <input type="checkbox"/> Countersink <input type="checkbox"/> Cut Too Short <input type="checkbox"/> Drill Holes <input type="checkbox"/> Drawing <input type="checkbox"/> Finish <input type="checkbox"/> Folio | <input type="checkbox"/> Grain <input type="checkbox"/> Hardware <input type="checkbox"/> Inspection Incomplete <input type="checkbox"/> Instructions Incomplete/Unclear <input type="checkbox"/> Maintenance <input type="checkbox"/> Mislabeled <input type="checkbox"/> Misread <input type="checkbox"/> Offset <input type="checkbox"/> Out of Calibration <input type="checkbox"/> Out of Sequence <input type="checkbox"/> Outside Dimensions <input type="checkbox"/> Ovalized <input type="checkbox"/> Over/Under tolerance <input type="checkbox"/> Part Incorrect <input type="checkbox"/> Part Lost/Missing <input type="checkbox"/> Part Moved <input type="checkbox"/> Positioned Wrong <input type="checkbox"/> Power Loss/Surge <input type="checkbox"/> Pressure/Forced <input type="checkbox"/> Temperature/Cure <input type="checkbox"/> Weld <input type="checkbox"/> Wrong Stock Pulled <input type="checkbox"/> Other |
|--|---|--|

Work Order ID 93738***93738***

Page 5

November-27-12 10:47:43 AM

Item ID: D350-748-201

Accept

N900040100Setup Start ***NS1***

Revision ID:

Stop ***NS2***

Item Name: Crosstube Installation, High Aft

Start Date: 11/22/12 Start Qty: 1.00

1

Cust Item ID:

Required Date: 12/21/12 Req'd Qty: 1.00

1

Customer:

Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____

Run Start ***NR1***

QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Stop ***NR2***

| Sequence ID/ Work Center ID | Operation Description | Set Up/ Run Hours | Tool ID | Tool # | Plan Code | Accept Qty | Reject Qty | Reject Number | Insp. Stamp |
|--------------------------------|--------------------------|----------------------|---------|--------|--------------|---------------|---------------|------------------|----------------|
|--------------------------------|--------------------------|----------------------|---------|--------|--------------|---------------|---------------|------------------|----------------|

172

0.00

172


Crosstubes

Memo

0.00

Crosstubes

LOAD TEST TO 3000LB FOR 1 MINUTE



174

Outsource process - NDT per QSI038 4.1

0.00

174

Outsource2

Memo

0.00

Outsource process - NDT

P/O: 18679

C212112/20 ①

176

Receive & Inspect for Damage & Mat'l Certs

0.00


176

Packaging

Memo

0.00

Packaging



NCR: Yes / No

WORK ORDER NON-CONFORMANCE / UPDATE

DQA: _____ Date: _____

QA Closed: _____ Date: _____

| | | | | | | | | | | | |
|--|-------------|-------------|------------|---|--------------------------|---|------------------------|---------------------|---------------------|--|--|
| Work Order: _____ Part No. _____ NCR No. _____ | | | | DISPOSITION Rework <input type="checkbox"/> Scrap <input type="checkbox"/> Use-as-is <input type="checkbox"/> Work Order Update <input type="checkbox"/> | | AGAINST DEPARTMENT/PROCESS <div style="display: flex; justify-content: space-between;"> <div> Skid-tube <input type="checkbox"/> Machining <input type="checkbox"/> Thermoforming <input type="checkbox"/> Large Fab <input type="checkbox"/> </div> <div> Crosstube <input type="checkbox"/> Small Fab <input type="checkbox"/> Finishing <input type="checkbox"/> Composite <input type="checkbox"/> </div> <div> Water Jet <input type="checkbox"/> Prod. Eng. Coord. <input type="checkbox"/> Rec/Store/Packaging <input type="checkbox"/> Supplier <input type="checkbox"/> </div> <div> Engineering <input type="checkbox"/> Quality <input type="checkbox"/> Other <input type="checkbox"/> </div> </div> | | | | | |
| Root Cause | Date | Step | Qty | Description of work order update or Non-conformance | Initial Chief Eng | Action Description | Sign & Date | Verification | QC Inspector | | |
| Doc/Data <input type="checkbox"/> | | | | | | | | | | | |
| Equip/Tooling <input type="checkbox"/> | | | | | | | | | | | |
| Operator <input type="checkbox"/> | | | | | | | | | | | |
| Material <input type="checkbox"/> | | | | | | | | | | | |
| Setup <input type="checkbox"/> | | | | | | | | | | | |
| Other <input type="checkbox"/> | | | | | | | | | | | |
| Process <input type="checkbox"/> | | | | | | | | | | | |
| Supplier <input type="checkbox"/> | | | | | | | | | | | |
| Training <input type="checkbox"/> | | | | | | | | | | | |
| Unapproved <input type="checkbox"/> | | | | | | | | | | | |

| FAULT CATEGORY | | | | | | | | | |
|---|---|--|---|---|--|--|--|--|--|
| Landing Gear | | | General | | | | | | |
| <input type="checkbox"/> Bending | <input type="checkbox"/> Bend | <input type="checkbox"/> Grain | <input type="checkbox"/> Ovalized | <input type="checkbox"/> Pressure/Forced | | | | | |
| <input type="checkbox"/> Centre Not Concentric to O/S | <input type="checkbox"/> BOM/Route | <input type="checkbox"/> Hardware | <input type="checkbox"/> Over/Under tolerance | <input type="checkbox"/> Temperature/Cure | | | | | |
| <input type="checkbox"/> Cracks | <input type="checkbox"/> Broken/Damaged | <input type="checkbox"/> Inspection Incomplete | <input type="checkbox"/> Part Incorrect | <input type="checkbox"/> Weld | | | | | |
| <input type="checkbox"/> Crushed/Crimped | <input type="checkbox"/> Burrs | <input type="checkbox"/> Instructions Incomplete/Unclear | <input type="checkbox"/> Part Lost/Missing | <input type="checkbox"/> Wrong Stock Pulled | | | | | |
| <input type="checkbox"/> Cuffs | <input type="checkbox"/> Contamination | <input type="checkbox"/> Maintenance | <input type="checkbox"/> Part Moved | | | | | | |
| <input type="checkbox"/> Heat Treat | <input type="checkbox"/> Countersink | <input type="checkbox"/> Mislabeled | <input type="checkbox"/> Positioned Wrong | <input type="checkbox"/> Other | | | | | |
| <input type="checkbox"/> Inspection Strip in Tube | <input type="checkbox"/> Cut Too Short | <input type="checkbox"/> Misread | <input type="checkbox"/> Power Loss/Surge | | | | | | |
| <input type="checkbox"/> Ripples in Bend | <input type="checkbox"/> Drill Holes | <input type="checkbox"/> Offset | | | | | | | |
| <input type="checkbox"/> Torque Waves in Extrusion | <input type="checkbox"/> Drawing | <input type="checkbox"/> Out of Calibration | | | | | | | |
| <input type="checkbox"/> Turning Sequence | <input type="checkbox"/> Finish | <input type="checkbox"/> Out of Sequence | | | | | | | |
| <input type="checkbox"/> Wave/Twist in Tube | <input type="checkbox"/> Folio | <input type="checkbox"/> Outside Dimensions | | | | | | | |

Work Order ID 93738

93738

Page 6

November-27-12 10:47:43 AM

Item ID: D350-748-201

Accept

N900040100

Setup Start *NS1*

Revision ID:

Stop *NS2*

Item Name: Crosstube Installation, High Aft

Start Date: 11/22/12 Start Qty: 1.00 *1*

Cust Item ID:

Required Date: 12/21/12 Req'd Qty: 1.00 *1*

Customer:

Reference:

Run Start *NR1*

Approvals: Process Plan: Date: Tooling: Date:

Stop *NR2*

QC: Date: SPC (Y/N): Date:

| Sequence ID/ Work Center ID | Operation Description | Set Up/ Run Hours | Tool ID | Tool # | Plan Code | Accept Qty | Reject Qty | Reject Number | Insp. Stamp |
|--|--|---|---------|--------|--------------|---------------|---------------|------------------|----------------|
| 178 *178* QC Quality Control | QC5- Inspect part completeness to step on W/O Memo | 0.00 DAS 15 8-89 0.00 121200 | | | | 1 | | | |
| 180 *180* SprayPaint Spray Painting | SprayPaint Memo 1-Prime inside crosstube as per QSI 005 4.2 2-Paint Outside of Tube as per Dart QSI 005 4.2 | 0.00 0.00 122888 12:30-1:00 123591 5:00-5:45 | | | | 1 | 0 | 0 | AB 12-12-20 |
| 190 *190* QC Quality Control | QC14- Inspect Spray Paint Memo Then, Wrap in plastic bag to protect from scratches | 0.00 0.00 DAS 16 8-89 171221 | | | | | | | |

NCR: Yes / No

WORK ORDER NON-CONFORMANCE / UPDATE

DQA: _____ Date: _____

QA Closed: _____ Date: _____

| | | | | | | | | | | | | | | | | | | |
|--|---|---|--------------------------------------|------------------------------------|------------------------------------|--------------------------------------|------------------------------------|------------------------------------|--|----------------------------------|--|------------------------------------|--|--------------------------------|------------------------------------|------------------------------------|-----------------------------------|--|
| Work Order: _____ Part No. _____ NCR No. _____ | DISPOSITION Rework <input type="checkbox"/> Scrap <input type="checkbox"/> Use-as-is <input type="checkbox"/> Work Order Update <input type="checkbox"/> | AGAINST DEPARTMENT/PROCESS <table style="width: 100%;"> <tr> <td>Skid-tube <input type="checkbox"/></td> <td>Crosstube <input type="checkbox"/></td> <td>Water Jet <input type="checkbox"/></td> <td>Engineering <input type="checkbox"/></td> </tr> <tr> <td>Machining <input type="checkbox"/></td> <td>Small Fab <input type="checkbox"/></td> <td>Prod. Eng. Coord. <input type="checkbox"/></td> <td>Quality <input type="checkbox"/></td> </tr> <tr> <td>Thermoforming <input type="checkbox"/></td> <td>Finishing <input type="checkbox"/></td> <td>Rec/Store/Packaging <input type="checkbox"/></td> <td>Other <input type="checkbox"/></td> </tr> <tr> <td>Large Fab <input type="checkbox"/></td> <td>Composite <input type="checkbox"/></td> <td>Supplier <input type="checkbox"/></td> <td></td> </tr> </table> | Skid-tube <input type="checkbox"/> | Crosstube <input type="checkbox"/> | Water Jet <input type="checkbox"/> | Engineering <input type="checkbox"/> | Machining <input type="checkbox"/> | Small Fab <input type="checkbox"/> | Prod. Eng. Coord. <input type="checkbox"/> | Quality <input type="checkbox"/> | Thermoforming <input type="checkbox"/> | Finishing <input type="checkbox"/> | Rec/Store/Packaging <input type="checkbox"/> | Other <input type="checkbox"/> | Large Fab <input type="checkbox"/> | Composite <input type="checkbox"/> | Supplier <input type="checkbox"/> | |
| Skid-tube <input type="checkbox"/> | Crosstube <input type="checkbox"/> | Water Jet <input type="checkbox"/> | Engineering <input type="checkbox"/> | | | | | | | | | | | | | | | |
| Machining <input type="checkbox"/> | Small Fab <input type="checkbox"/> | Prod. Eng. Coord. <input type="checkbox"/> | Quality <input type="checkbox"/> | | | | | | | | | | | | | | | |
| Thermoforming <input type="checkbox"/> | Finishing <input type="checkbox"/> | Rec/Store/Packaging <input type="checkbox"/> | Other <input type="checkbox"/> | | | | | | | | | | | | | | | |
| Large Fab <input type="checkbox"/> | Composite <input type="checkbox"/> | Supplier <input type="checkbox"/> | | | | | | | | | | | | | | | | |

| Root Cause | Date | Step | Qty | Description of work order update or Non-conformance | Initial Chief Eng | Action Description | Sign & Date | Verification | QC Inspector |
|---------------|------|------|-----|---|-------------------|--------------------|-------------|--------------|--------------|
| Doc/Data | | | | | | | | | |
| Equip/Tooling | | | | | | | | | |
| Operator | | | | | | | | | |
| Material | | | | | | | | | |
| Setup | | | | | | | | | |
| Other | | | | | | | | | |
| Process | | | | | | | | | |
| Supplier | | | | | | | | | |
| Training | | | | | | | | | |
| Unapproved | | | | | | | | | |

FAULT CATEGORY

| Landing Gear | General | Other |
|---|---|--|
| <input type="checkbox"/> Bending | <input type="checkbox"/> Bend | <input type="checkbox"/> Grain |
| <input type="checkbox"/> Centre Not Concentric to O/S | <input type="checkbox"/> BOM/Route | <input type="checkbox"/> Hardware |
| <input type="checkbox"/> Cracks | <input type="checkbox"/> Broken/Damaged | <input type="checkbox"/> Inspection Incomplete |
| <input type="checkbox"/> Crushed/Crimped | <input type="checkbox"/> Burrs | <input type="checkbox"/> Instructions Incomplete/Unclear |
| <input type="checkbox"/> Cuffs | <input type="checkbox"/> Contamination | <input type="checkbox"/> Maintenance |
| <input type="checkbox"/> Heat Treat | <input type="checkbox"/> Countersink | <input type="checkbox"/> Mislabeled |
| <input type="checkbox"/> Inspection Strip in Tube | <input type="checkbox"/> Cut Too Short | <input type="checkbox"/> Misread |
| <input type="checkbox"/> Ripples in Bend | <input type="checkbox"/> Drill Holes | <input type="checkbox"/> Offset |
| <input type="checkbox"/> Torque Waves in Extrusion | <input type="checkbox"/> Drawing | <input type="checkbox"/> Out of Calibration |
| <input type="checkbox"/> Turning Sequence | <input type="checkbox"/> Finish | <input type="checkbox"/> Out of Sequence |
| <input type="checkbox"/> Wave/Twist in Tube | <input type="checkbox"/> Folio | <input type="checkbox"/> Outside Dimensions |
| | | <input type="checkbox"/> Ovalized |
| | | <input type="checkbox"/> Over/Under tolerance |
| | | <input type="checkbox"/> Part Incorrect |
| | | <input type="checkbox"/> Part Lost/Missing |
| | | <input type="checkbox"/> Part Moved |
| | | <input type="checkbox"/> Positioned Wrong |
| | | <input type="checkbox"/> Power Loss/Surge |
| | | <input type="checkbox"/> Pressure/Forced |
| | | <input type="checkbox"/> Temperature/Cure |
| | | <input type="checkbox"/> Weld |
| | | <input type="checkbox"/> Wrong Stock Pulled |
| | | <input type="checkbox"/> Other |

Work Order ID 93738***93738***

Page 7

November-27-12 10:47:43 AM

Item ID: D350-748-201

Accept

N900040100Setup Start ***NS1***

Revision ID:

Stop ***NS2***

Item Name: Crosstube Installation, High Aft

Start Date: 11/22/12 Start Qty: 1.00

1

Cust Item ID:

Required Date: 12/21/12 Req'd Qty: 1.00

1

Customer:

Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____

Run Start ***NR1***

QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Stop ***NR2***

| Sequence ID/ Work Center ID | Operation Description | Set Up/ Run Hours | Tool ID | Tool # | Plan Code | Accept Qty | Reject Qty | Reject Number | Insp. Stamp |
|--------------------------------|--------------------------|----------------------|---------|--------|--------------|---------------|---------------|------------------|----------------|
|--------------------------------|--------------------------|----------------------|---------|--------|--------------|---------------|---------------|------------------|----------------|

200

0.00

200

Crosstubes

Crosstubes

Memo

0.00

Crosstubes

1-Install Ground wire Insert, then insert screw and washer

2-Abrade mating surfaces of support and crosstube with 400 grit sandpaper,
clean the area with 4105S wash 'n' wipe3-Install supports with Proseal 890 per and QSI 015
A/R Proseal 890 Batch: _____4-Install supports clamps Using Dt8876 as per Dwg D350-748-241, Torque to
60-80 IN-LBS

Install Abrasion strips as per Dwg D350-748-241 + QSI 015

Install supports using Dt8876

Torque to 60-80 in LBS

12-12-21

210

QC5- Inspect part completeness to step on W/O

0.00

210

QC

Quality Control

Memo

0.00

DAS
15
12-12-21DAS
15
12-12-21

NCR: Yes / No

WORK ORDER NON-CONFORMANCE / UPDATE

DQA: _____ Date: _____

QA Closed: _____ Date: _____

| | | | | | | | | | | | |
|--|----------|------|-----|--|-------------------|---|-------------|--------------|--------------|--|--|
| Work Order: _____ Part No. _____ NCR No. _____ | | | | DISPOSITION Rework <input type="checkbox"/> Scrap <input type="checkbox"/> Use-as-is <input type="checkbox"/> Work Order Update <input checked="" type="checkbox"/> | | AGAINST DEPARTMENT/PROCESS <div style="display: flex; justify-content: space-between;"> <div> Skid-tube <input type="checkbox"/> Machining <input type="checkbox"/> Thermoforming <input type="checkbox"/> Large Fab <input type="checkbox"/> </div> <div> Crosstube <input type="checkbox"/> Small Fab <input type="checkbox"/> Finishing <input type="checkbox"/> Composite <input type="checkbox"/> </div> <div> Water Jet <input type="checkbox"/> Prod. Eng. Coord. <input type="checkbox"/> Rec/Store/Packaging <input type="checkbox"/> Supplier <input type="checkbox"/> </div> <div> Engineering <input type="checkbox"/> Quality <input type="checkbox"/> Other <input type="checkbox"/> </div> </div> | | | | | |
| THIS W/O ONLY | | | | | | | | | | | |
| Root Cause | Date | Step | Qty | Description of work order update or Non-conformance | Initial Chief Eng | Action Description | Sign & Date | Verification | QC Inspector | | |
| Doc/Data <input type="checkbox"/> | 12/12/21 | 210 | 1 | Assemble per DSSG-74E-241 Rev. F | 12/12/21 | MS21920-20 <u>B/N</u> DZ656-400-710 | | | | | |
| Equip/Tooling <input type="checkbox"/> | | | | | | | | | | | |
| Operator <input type="checkbox"/> | | | | | | | | | | | |
| Material <input type="checkbox"/> | | | | | | | | | | | |
| Setup <input type="checkbox"/> | | | | | | | | | | | |
| Other <input type="checkbox"/> | | | | | | | | | | | |
| Process <input type="checkbox"/> | | | | | | | | | | | |
| Supplier <input type="checkbox"/> | | | | | | | | | | | |
| Training <input type="checkbox"/> | | | | | | | | | | | |
| Unapproved <input type="checkbox"/> | | | | | | | | | | | |

| FAULT CATEGORY | | | |
|--|---|---|---|
| Landing Gear <input type="checkbox"/> Bending <input type="checkbox"/> Centre Not Concentric to O/S <input type="checkbox"/> Cracks <input type="checkbox"/> Crushed/Crimped. <input type="checkbox"/> Cuffs <input type="checkbox"/> Heat Treat <input type="checkbox"/> Inspection Strip in Tube <input type="checkbox"/> Ripples in Bend <input type="checkbox"/> Torque Waves in Extrusion <input type="checkbox"/> Turning Sequence <input type="checkbox"/> Wave/Twist in Tube | General <input type="checkbox"/> Bend <input type="checkbox"/> BOM/Route <input type="checkbox"/> Broken/Damaged <input type="checkbox"/> Burrs <input type="checkbox"/> Contamination <input type="checkbox"/> Countersink <input type="checkbox"/> Cut Too Short <input type="checkbox"/> Drill Holes <input type="checkbox"/> Drawing <input type="checkbox"/> Finish <input type="checkbox"/> Folio | <input type="checkbox"/> Grain <input type="checkbox"/> Hardware <input type="checkbox"/> Inspection Incomplete <input type="checkbox"/> Instructions Incomplete/Unclear <input type="checkbox"/> Maintenance <input type="checkbox"/> Mislabeled <input type="checkbox"/> Misread <input type="checkbox"/> Offset <input type="checkbox"/> Out of Calibration <input type="checkbox"/> Out of Sequence <input type="checkbox"/> Outside Dimensions | <input type="checkbox"/> Ovalized <input type="checkbox"/> Over/Under tolerance <input type="checkbox"/> Part Incorrect <input type="checkbox"/> Part Lost/Missing <input type="checkbox"/> Part Moved <input type="checkbox"/> Positioned Wrong <input type="checkbox"/> Power Loss/Surge <input type="checkbox"/> Pressure/Forced <input type="checkbox"/> Temperature/Cure <input type="checkbox"/> Weld <input type="checkbox"/> Wrong Stock Pulled <input type="checkbox"/> Other |

Work Order ID 93738

93738

Page 8

November-27-12 10:47:43 AM

Item ID: D350-748-201

Accept

N900040100

Setup Start *NS1*

Revision ID:

Stop *NS2*

Item Name: Crosstube Installation, High Aft

Start Date: 11/22/12 Start Qty: 1.00

1

Cust Item ID:

Required Date: 12/21/12 Req'd Qty: 1.00

1

Customer:

Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____

Run Start *NR1*

QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Stop *NR2*

| Sequence ID/ Work Center ID | Operation Description | Set Up/ Run Hours | Tool ID | Tool # | Plan Code | Accept Qty | Reject Qty | Reject Number | Insp. Stamp |
|--------------------------------|---|----------------------|---------|--------|--------------|---------------|---------------|------------------|----------------|
| 220 | Pick Kit | 0.00 | | | | | | | |
| *220* | | | | | | 1X | | | SD |
| Packaging | Memo | 0.00 | | | | | | | 12/12/20 |
| Packaging | | | | | | | | | |
| 230 | QC4- 100% Inspect kits for completeness | 0.00 | | | | | | | |
| *230* | | | | | | | | | |
| QC | Memo | 0.00 | | | | | | | 12/12/21 |
| Quality Control | | | | | | | | | |
| 240 | | 0.00 | | | | | | | |
| *240* | Packaging | | | | | | | | |
| Packaging | Memo | 0.00 | | | | | | | SL 12/12/21 |
| Packaging | Identify and pack for shipping as per PPPD350-748-201 | | | | | | | | |
| | Location: SHIP | | | | | | | | |
| | PPP Rev: | | | | | | | | |

NCR: Yes / No

WORK ORDER NON-CONFORMANCE / UPDATE

DQA: _____ Date: _____

QA Closed: _____ Date: _____

| | | | | | | | | | | | | | | | | | | |
|--|---|---|--------------------------------------|------------------------------------|------------------------------------|--------------------------------------|------------------------------------|------------------------------------|--|----------------------------------|--|------------------------------------|--|--------------------------------|------------------------------------|------------------------------------|-----------------------------------|--|
| Work Order: _____ Part No. _____ NCR No. _____ | DISPOSITION Rework <input type="checkbox"/> Scrap <input type="checkbox"/> Use-as-is <input type="checkbox"/> Work Order Update <input type="checkbox"/> | AGAINST DEPARTMENT/PROCESS <table style="width: 100%; border: none;"> <tr> <td style="width: 25%;">Skid-tube <input type="checkbox"/></td> <td style="width: 25%;">Crosstube <input type="checkbox"/></td> <td style="width: 25%;">Water Jet <input type="checkbox"/></td> <td style="width: 25%;">Engineering <input type="checkbox"/></td> </tr> <tr> <td>Machining <input type="checkbox"/></td> <td>Small Fab <input type="checkbox"/></td> <td>Prod. Eng. Coord. <input type="checkbox"/></td> <td>Quality <input type="checkbox"/></td> </tr> <tr> <td>Thermoforming <input type="checkbox"/></td> <td>Finishing <input type="checkbox"/></td> <td>Rec/Store/Packaging <input type="checkbox"/></td> <td>Other <input type="checkbox"/></td> </tr> <tr> <td>Large Fab <input type="checkbox"/></td> <td>Composite <input type="checkbox"/></td> <td>Supplier <input type="checkbox"/></td> <td></td> </tr> </table> | Skid-tube <input type="checkbox"/> | Crosstube <input type="checkbox"/> | Water Jet <input type="checkbox"/> | Engineering <input type="checkbox"/> | Machining <input type="checkbox"/> | Small Fab <input type="checkbox"/> | Prod. Eng. Coord. <input type="checkbox"/> | Quality <input type="checkbox"/> | Thermoforming <input type="checkbox"/> | Finishing <input type="checkbox"/> | Rec/Store/Packaging <input type="checkbox"/> | Other <input type="checkbox"/> | Large Fab <input type="checkbox"/> | Composite <input type="checkbox"/> | Supplier <input type="checkbox"/> | |
| Skid-tube <input type="checkbox"/> | Crosstube <input type="checkbox"/> | Water Jet <input type="checkbox"/> | Engineering <input type="checkbox"/> | | | | | | | | | | | | | | | |
| Machining <input type="checkbox"/> | Small Fab <input type="checkbox"/> | Prod. Eng. Coord. <input type="checkbox"/> | Quality <input type="checkbox"/> | | | | | | | | | | | | | | | |
| Thermoforming <input type="checkbox"/> | Finishing <input type="checkbox"/> | Rec/Store/Packaging <input type="checkbox"/> | Other <input type="checkbox"/> | | | | | | | | | | | | | | | |
| Large Fab <input type="checkbox"/> | Composite <input type="checkbox"/> | Supplier <input type="checkbox"/> | | | | | | | | | | | | | | | | |

| Root Cause | Date | Step | Qty | Description of work order update or Non-conformance | Initial Chief Eng | Action Description | Sign & Date | Verification | QC Inspector |
|--|------|------|-----|---|-------------------|--------------------|-------------|--------------|--------------|
| Doc/Data <input type="checkbox"/> | | | | | | | | | |
| Equip/Tooling <input type="checkbox"/> | | | | | | | | | |
| Operator <input type="checkbox"/> | | | | | | | | | |
| Material <input type="checkbox"/> | | | | | | | | | |
| Setup <input type="checkbox"/> | | | | | | | | | |
| Other <input type="checkbox"/> | | | | | | | | | |
| Process <input type="checkbox"/> | | | | | | | | | |
| Supplier <input type="checkbox"/> | | | | | | | | | |
| Training <input type="checkbox"/> | | | | | | | | | |
| Unapproved <input type="checkbox"/> | | | | | | | | | |

FAULT CATEGORY

| | | |
|--|---|--|
| Landing Gear <input type="checkbox"/> Bending <input type="checkbox"/> Centre Not Concentric to O/S <input type="checkbox"/> Cracks <input type="checkbox"/> Crushed/Crimped. <input type="checkbox"/> Cuffs <input type="checkbox"/> Heat Treat <input type="checkbox"/> Inspection Strip in Tube <input type="checkbox"/> Ripples in Bend <input type="checkbox"/> Torque Waves in Extrusion <input type="checkbox"/> Turning Sequence <input type="checkbox"/> Wave/Twist in Tube | General <input type="checkbox"/> Bend <input type="checkbox"/> BOM/Route <input type="checkbox"/> Broken/Damaged <input type="checkbox"/> Burrs <input type="checkbox"/> Contamination <input type="checkbox"/> Countersink <input type="checkbox"/> Cut Too Short <input type="checkbox"/> Drill Holes <input type="checkbox"/> Drawing <input type="checkbox"/> Finish <input type="checkbox"/> Folio | <input type="checkbox"/> Grain <input type="checkbox"/> Hardware <input type="checkbox"/> Inspection Incomplete <input type="checkbox"/> Instructions Incomplete/Unclear <input type="checkbox"/> Maintenance <input type="checkbox"/> Mislabeled <input type="checkbox"/> Misread <input type="checkbox"/> Offset <input type="checkbox"/> Out of Calibration <input type="checkbox"/> Out of Sequence <input type="checkbox"/> Outside Dimensions <input type="checkbox"/> Ovalized <input type="checkbox"/> Over/Under tolerance <input type="checkbox"/> Part Incorrect <input type="checkbox"/> Part Lost/Missing <input type="checkbox"/> Part Moved <input type="checkbox"/> Positioned Wrong <input type="checkbox"/> Power Loss/Surge <input type="checkbox"/> Pressure/Forced <input type="checkbox"/> Temperature/Cure <input type="checkbox"/> Weld <input type="checkbox"/> Wrong Stock Pulled <input type="checkbox"/> Other |
|--|---|--|

Work Order ID 93738***93738***

Page 9

November-27-12 10:47:43 AM

Item ID: D350-748-201

Accept

N900040100Setup Start ***NS1***

Revision ID:

Stop ***NS2***

Item Name: Crosstube Installation, High Aft

Start Date: 11/22/12 Start Qty: 1.00

1

Cust Item ID:

Required Date: 12/21/12 Req'd Qty: 1.00

1

Customer:

Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____

Run Start ***NR1***

QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Stop ***NR2***

| Sequence ID/ Work Center ID | Operation Description | Set Up/ Run Hours | Tool ID | Tool # | Plan Code | Accept Qty | Reject Qty | Reject Number | Insp. Stamp |
|--------------------------------|---|----------------------|---------|--------|--------------|---------------|---------------|------------------|----------------|
| 250 | QC21- Final Inspection - Work Order Release | 0.00 | | | | | | | |
| *250* | | | | | | | | | |
| QC | Memo | 0.00 | | | | | | | |
| Quality Control | | | | | | | | | |

CK 12/12/12

MF 12-12-21

NCR: Yes / No

WORK ORDER NON-CONFORMANCE / UPDATE

DQA: _____ Date: _____

QA Closed: _____ Date: _____

| | | | | | | | | | | | | | | | | | | |
|--|---|---|--------------------------------------|------------------------------------|------------------------------------|--------------------------------------|------------------------------------|------------------------------------|--|----------------------------------|--|------------------------------------|--|--------------------------------|------------------------------------|------------------------------------|-----------------------------------|--|
| Work Order: _____ Part No. _____ NCR No. _____ | DISPOSITION Rework <input type="checkbox"/> Scrap <input type="checkbox"/> Use-as-is <input type="checkbox"/> Work Order Update <input type="checkbox"/> | AGAINST DEPARTMENT/PROCESS <table style="width: 100%;"> <tr> <td>Skid-tube <input type="checkbox"/></td> <td>Crosstube <input type="checkbox"/></td> <td>Water Jet <input type="checkbox"/></td> <td>Engineering <input type="checkbox"/></td> </tr> <tr> <td>Machining <input type="checkbox"/></td> <td>Small Fab <input type="checkbox"/></td> <td>Prod. Eng. Coord. <input type="checkbox"/></td> <td>Quality <input type="checkbox"/></td> </tr> <tr> <td>Thermoforming <input type="checkbox"/></td> <td>Finishing <input type="checkbox"/></td> <td>Rec/Store/Packaging <input type="checkbox"/></td> <td>Other <input type="checkbox"/></td> </tr> <tr> <td>Large Fab <input type="checkbox"/></td> <td>Composite <input type="checkbox"/></td> <td>Supplier <input type="checkbox"/></td> <td></td> </tr> </table> | Skid-tube <input type="checkbox"/> | Crosstube <input type="checkbox"/> | Water Jet <input type="checkbox"/> | Engineering <input type="checkbox"/> | Machining <input type="checkbox"/> | Small Fab <input type="checkbox"/> | Prod. Eng. Coord. <input type="checkbox"/> | Quality <input type="checkbox"/> | Thermoforming <input type="checkbox"/> | Finishing <input type="checkbox"/> | Rec/Store/Packaging <input type="checkbox"/> | Other <input type="checkbox"/> | Large Fab <input type="checkbox"/> | Composite <input type="checkbox"/> | Supplier <input type="checkbox"/> | |
| Skid-tube <input type="checkbox"/> | Crosstube <input type="checkbox"/> | Water Jet <input type="checkbox"/> | Engineering <input type="checkbox"/> | | | | | | | | | | | | | | | |
| Machining <input type="checkbox"/> | Small Fab <input type="checkbox"/> | Prod. Eng. Coord. <input type="checkbox"/> | Quality <input type="checkbox"/> | | | | | | | | | | | | | | | |
| Thermoforming <input type="checkbox"/> | Finishing <input type="checkbox"/> | Rec/Store/Packaging <input type="checkbox"/> | Other <input type="checkbox"/> | | | | | | | | | | | | | | | |
| Large Fab <input type="checkbox"/> | Composite <input type="checkbox"/> | Supplier <input type="checkbox"/> | | | | | | | | | | | | | | | | |

| Root Cause | Date | Step | Qty | Description of work order update or Non-conformance | Initial Chief Eng | Action Description | Sign & Date | Verification | QC Inspector |
|--|------|------|-----|---|-------------------|--------------------|-------------|--------------|--------------|
| Doc/Data <input type="checkbox"/> | | | | | | | | | |
| Equip/Tooling <input type="checkbox"/> | | | | | | | | | |
| Operator <input type="checkbox"/> | | | | | | | | | |
| Material <input type="checkbox"/> | | | | | | | | | |
| Setup <input type="checkbox"/> | | | | | | | | | |
| Other <input type="checkbox"/> | | | | | | | | | |
| Process <input type="checkbox"/> | | | | | | | | | |
| Supplier <input type="checkbox"/> | | | | | | | | | |
| Training <input type="checkbox"/> | | | | | | | | | |
| Unapproved <input type="checkbox"/> | | | | | | | | | |

FAULT CATEGORY

| | | |
|--|---|---|
| Landing Gear <input type="checkbox"/> Bending <input type="checkbox"/> Centre Not Concentric to O/S <input type="checkbox"/> Cracks <input type="checkbox"/> Crushed/Crimped. <input type="checkbox"/> Cuffs <input type="checkbox"/> Heat Treat <input type="checkbox"/> Inspection Strip in Tube <input type="checkbox"/> Ripples in Bend <input type="checkbox"/> Torque Waves in Extrusion <input type="checkbox"/> Turning Sequence <input type="checkbox"/> Wave/Twist in Tube | General <input type="checkbox"/> Bend <input type="checkbox"/> BOM/Route <input type="checkbox"/> Broken/Damaged <input type="checkbox"/> Burrs <input type="checkbox"/> Contamination <input type="checkbox"/> Countersink <input type="checkbox"/> Cut Too Short <input type="checkbox"/> Drill Holes <input type="checkbox"/> Drawing <input type="checkbox"/> Finish <input type="checkbox"/> Folio | <input type="checkbox"/> Grain <input type="checkbox"/> Hardware <input type="checkbox"/> Inspection Incomplete <input type="checkbox"/> Instructions Incomplete/Unclear <input type="checkbox"/> Maintenance <input type="checkbox"/> Mislabeled <input type="checkbox"/> Misread <input type="checkbox"/> Offset <input type="checkbox"/> Out of Calibration <input type="checkbox"/> Out of Sequence <input type="checkbox"/> Outside Dimensions |
| | | <input type="checkbox"/> Ovalized <input type="checkbox"/> Over/Under tolerance <input type="checkbox"/> Part Incorrect <input type="checkbox"/> Part Lost/Missing <input type="checkbox"/> Part Moved <input type="checkbox"/> Positioned Wrong <input type="checkbox"/> Power Loss/Surge |
| | | <input type="checkbox"/> Pressure/Forced <input type="checkbox"/> Temperature/Cure <input type="checkbox"/> Weld <input type="checkbox"/> Wrong Stock Pulled <input type="checkbox"/> Other |

Picklist Print

November-27-12 10:47:41 AM

Page 1

Work Order ID: 93738
 Parent Item: D350-748-201
 Parent Item Name: Crosstube Installation, High Aft

Start Date: 11/22/12
 Start Qty: 1.00

Required Date: 12/21/12
 Required Qty: 1.00

Comments:
 IPP Rev: A New Issue 06-07-05 JLM
 IPP Rev: B Update qty of MS21042L5 06-09-12 KJ
 IPP Rev C Combined manufacturing 08.04.02 EC verified by: DD
 IPP Rev:D 08-06-24 revD as per dwg DD verified by:EC
 IPP Rev: E 08.12.11 Step17 was step 21 KJ Verified by:EC IPP Rev:F 10.08.04 added QSI010
 4.3 DD verf:EC IPP REV:G ADD UNDER BEND COMMENT 12-05-28 JLM IPP
 REV:H 12.11.05 as per dwg D350-748-141G DD verf:JLM

| Component Item ID/ Item Name | Replacement Item ID | Mfg/ Purch | Bin Item | Primary Location | Last Location | Route Seq ID | Unit of Measure | Qty on Hand | Qty per Kit | Total Qty | Qty Issued | Date Issued | Status |
|---------------------------------|------------------------|---------------|-------------|---------------------|------------------|-----------------|--------------------|----------------|-------------|--------------|---------------|----------------|--------|
| ALS4-1032-225 Insert | | Purchased | No | | | 200 | Each | 1,687.0000 | 1 | 1 | | 12-12-21 | |
| | | | | <u>Location</u> | | <u>Loc Qty</u> | <u>Loc Code</u> | | | | | | |
| | | | | ST279 | | 1687 | | | | | | | |
| | | | | 108696 | | 146 | | | | | | | |
| | | | | 110768 | | 62 | | | | | | | |
| | | | | 118386 | | 55 | | | | | | | |
| | | | | 118966 | | 68 | | | | | | | |
| | | | | 120410 | | 10 | | | | | | | |
| | | | | 120451 | | 13 | | | | | | | |
| | | | | 121269 | | 77 | | | | | | | |
| | | | | 122290 | | 256 | | | | | | | |
| | | | | 122827 | | 1000 | | | | | | | |
| ALS4-11A Bolt | | Purchased | No | | | 220 | Each | 423.0000 | 8 | 8 | | 12/12/21 | |
| | | | | <u>Location</u> | | <u>Loc Qty</u> | <u>Loc Code</u> | | | | | | |
| | | | | 360 | | 181 | | | | | | | |
| | | | | 121185 | | 181 | | | | | | | |
| | | | | ST359 | | 242 | | | | | | | |
| | | | | 115108 | | 3 | | | | | | | |
| | | | | 119328 | | 5 | | | | | | | |
| | | | | 120423 | | 150 | | | | | | | |
| | | | | 123346 | | 84 | | | | | | | |

123346

NCR: Yes / No

WORK ORDER NON-CONFORMANCE / UPDATE

DQA: _____ Date: _____

QA Closed: _____ Date: _____

| | | | | | | | | | | | | | | | | | | |
|--|---|---|--------------------------------------|------------------------------------|------------------------------------|--------------------------------------|------------------------------------|------------------------------------|--|----------------------------------|--|------------------------------------|--|--------------------------------|------------------------------------|------------------------------------|-----------------------------------|--|
| Work Order: _____ Part No. _____ NCR No. _____ | DISPOSITION Rework <input type="checkbox"/> Scrap <input type="checkbox"/> Use-as-is <input type="checkbox"/> Work Order Update <input type="checkbox"/> | AGAINST DEPARTMENT/PROCESS <table style="width: 100%;"> <tr> <td>Skid-tube <input type="checkbox"/></td> <td>Crosstube <input type="checkbox"/></td> <td>Water Jet <input type="checkbox"/></td> <td>Engineering <input type="checkbox"/></td> </tr> <tr> <td>Machining <input type="checkbox"/></td> <td>Small Fab <input type="checkbox"/></td> <td>Prod. Eng. Coord. <input type="checkbox"/></td> <td>Quality <input type="checkbox"/></td> </tr> <tr> <td>Thermoforming <input type="checkbox"/></td> <td>Finishing <input type="checkbox"/></td> <td>Rec/Store/Packaging <input type="checkbox"/></td> <td>Other <input type="checkbox"/></td> </tr> <tr> <td>Large Fab <input type="checkbox"/></td> <td>Composite <input type="checkbox"/></td> <td>Supplier <input type="checkbox"/></td> <td></td> </tr> </table> | Skid-tube <input type="checkbox"/> | Crosstube <input type="checkbox"/> | Water Jet <input type="checkbox"/> | Engineering <input type="checkbox"/> | Machining <input type="checkbox"/> | Small Fab <input type="checkbox"/> | Prod. Eng. Coord. <input type="checkbox"/> | Quality <input type="checkbox"/> | Thermoforming <input type="checkbox"/> | Finishing <input type="checkbox"/> | Rec/Store/Packaging <input type="checkbox"/> | Other <input type="checkbox"/> | Large Fab <input type="checkbox"/> | Composite <input type="checkbox"/> | Supplier <input type="checkbox"/> | |
| Skid-tube <input type="checkbox"/> | Crosstube <input type="checkbox"/> | Water Jet <input type="checkbox"/> | Engineering <input type="checkbox"/> | | | | | | | | | | | | | | | |
| Machining <input type="checkbox"/> | Small Fab <input type="checkbox"/> | Prod. Eng. Coord. <input type="checkbox"/> | Quality <input type="checkbox"/> | | | | | | | | | | | | | | | |
| Thermoforming <input type="checkbox"/> | Finishing <input type="checkbox"/> | Rec/Store/Packaging <input type="checkbox"/> | Other <input type="checkbox"/> | | | | | | | | | | | | | | | |
| Large Fab <input type="checkbox"/> | Composite <input type="checkbox"/> | Supplier <input type="checkbox"/> | | | | | | | | | | | | | | | | |

| Root Cause | Date | Step | Qty | Description of work order update or Non-conformance | Initial Chief Eng | Action Description | Sign & Date | Verification | QC Inspector |
|--|------|------|-----|---|-------------------|--------------------|-------------|--------------|--------------|
| Doc/Data <input type="checkbox"/> | | | | | | | | | |
| Equip/Tooling <input type="checkbox"/> | | | | | | | | | |
| Operator <input type="checkbox"/> | | | | | | | | | |
| Material <input type="checkbox"/> | | | | | | | | | |
| Setup <input type="checkbox"/> | | | | | | | | | |
| Other <input type="checkbox"/> | | | | | | | | | |
| Process <input type="checkbox"/> | | | | | | | | | |
| Supplier <input type="checkbox"/> | | | | | | | | | |
| Training <input type="checkbox"/> | | | | | | | | | |
| Unapproved <input type="checkbox"/> | | | | | | | | | |

FAULT CATEGORY

| | | |
|--|---|--|
| Landing Gear <input type="checkbox"/> Bending <input type="checkbox"/> Centre Not Concentric to O/S <input type="checkbox"/> Cracks <input type="checkbox"/> Crushed/Crimped. <input type="checkbox"/> Cuffs <input type="checkbox"/> Heat Treat <input type="checkbox"/> Inspection Strip in Tube <input type="checkbox"/> Ripples in Bend <input type="checkbox"/> Torque Waves in Extrusion <input type="checkbox"/> Turning Sequence <input type="checkbox"/> Wave/Twist in Tube | General <input type="checkbox"/> Bend <input type="checkbox"/> BOM/Route <input type="checkbox"/> Broken/Damaged <input type="checkbox"/> Burrs <input type="checkbox"/> Contamination <input type="checkbox"/> Countersink <input type="checkbox"/> Cut Too Short <input type="checkbox"/> Drill Holes <input type="checkbox"/> Drawing <input type="checkbox"/> Finish <input type="checkbox"/> Folio | <input type="checkbox"/> Grain <input type="checkbox"/> Hardware <input type="checkbox"/> Inspection Incomplete <input type="checkbox"/> Instructions Incomplete/Unclear <input type="checkbox"/> Maintenance <input type="checkbox"/> Mislabeled <input type="checkbox"/> Misread <input type="checkbox"/> Offset <input type="checkbox"/> Out of Calibration <input type="checkbox"/> Out of Sequence <input type="checkbox"/> Outside Dimensions <input type="checkbox"/> Ovalized <input type="checkbox"/> Over/Under tolerance <input type="checkbox"/> Part Incorrect <input type="checkbox"/> Part Lost/Missing <input type="checkbox"/> Part Moved <input type="checkbox"/> Positioned Wrong <input type="checkbox"/> Power Loss/Surge <input type="checkbox"/> Pressure/Forced <input type="checkbox"/> Temperature/Cure <input type="checkbox"/> Weld <input type="checkbox"/> Wrong Stock Pulled <input type="checkbox"/> Other |
|--|---|--|

Picklist Print

November-27-12 10:47:41 AM

Page 2

Work Order ID: 93738

Parent Item: D350-748-201

Parent Item Name: Crosstube Installation, High Aft

Start Date: 11/22/12

Required Date: 12/21/12

Start Qty: 1.00

Required Qty: 1.00

AN4-6A Purchased No

220 Each 3,857.0000

16

16

Bolt

Location

Loc Qty

Loc Code

ST355

3857

121243

2

123248

5

123355

3850

Purchased No

220 Each 279.0000

AN5-32A

Bolt

Location

Loc Qty

Loc Code

ST337

278

121541

5

122151

93

122416

50

122800

50

123522

80

ST338

1

122993

1

AN960JD10

Washer

NAS1149D0363J

Purchased

No

200 Each 0.0000

122378

AN960JD416

Washer

NAS1149D0463J

Purchased

No

220 Each 29.0000

Location

Loc Qty

Loc Code

ST351

29

116289

8

119097

21

AN960JD516

Washer

NAS1149D0563J

Purchased

No

220 Each 2.0000

Location

Loc Qty

Loc Code

ST338

2

1069059

2

November-27-12 10:47:41 AM

Shop Packet Print

Page 2

NCR: Yes / No

WORK ORDER NON-CONFORMANCE / UPDATE

DQA: _____ Date: _____

QA Closed: _____ Date: _____

| | | | | | | | | | | | |
|---|------|------|---|---|-------------------|---|-------------|--------------|--|--|---|
| Work Order: _____ Part No. _____ NCR No. _____ | | | | DISPOSITION Rework <input type="checkbox"/> Scrap <input type="checkbox"/> Use-as-is <input type="checkbox"/> Work Order Update <input type="checkbox"/> | | AGAINST DEPARTMENT/PROCESS <div style="display: flex; justify-content: space-between;"> <div> Skid-tube <input type="checkbox"/> Machining <input type="checkbox"/> Thermoforming <input type="checkbox"/> Large Fab <input type="checkbox"/> </div> <div> Crosstube <input type="checkbox"/> Small Fab <input type="checkbox"/> Finishing <input type="checkbox"/> Composite <input type="checkbox"/> </div> <div> Water Jet <input type="checkbox"/> Prod. Eng. Coord. <input type="checkbox"/> Rec/Store/Packaging <input type="checkbox"/> Supplier <input type="checkbox"/> </div> <div> Engineering <input type="checkbox"/> Quality <input type="checkbox"/> Other <input type="checkbox"/> </div> </div> | | | | | |
| Root Cause | Date | Step | Qty | Description of work order update or Non-conformance | Initial Chief Eng | Action Description | Sign & Date | Verification | QC Inspector | | |
| Doc/Data <input type="checkbox"/> | | | | | | | | | | | |
| Equip/Tooling <input type="checkbox"/> | | | | | | | | | | | |
| Operator <input type="checkbox"/> | | | | | | | | | | | |
| Material <input type="checkbox"/> | | | | | | | | | | | |
| Setup <input type="checkbox"/> | | | | | | | | | | | |
| Other <input type="checkbox"/> | | | | | | | | | | | |
| Process <input type="checkbox"/> | | | | | | | | | | | |
| Supplier <input type="checkbox"/> | | | | | | | | | | | |
| Training <input type="checkbox"/> | | | | | | | | | | | |
| Unapproved <input type="checkbox"/> | | | | | | | | | | | |
| FAULT CATEGORY | | | | | | | | | | | |
| Landing Gear <input type="checkbox"/> Bending <input type="checkbox"/> Centre Not Concentric to O/S <input type="checkbox"/> Cracks <input type="checkbox"/> Crushed/Crimped <input type="checkbox"/> Cuffs <input type="checkbox"/> Heat Treat <input type="checkbox"/> Inspection Strip in Tube <input type="checkbox"/> Ripples in Bend <input type="checkbox"/> Torque Waves in Extrusion <input type="checkbox"/> Turning Sequence <input type="checkbox"/> Wave/Twist in Tube | | | General <input type="checkbox"/> Bend <input type="checkbox"/> BOM/Route <input type="checkbox"/> Broken/Damaged <input type="checkbox"/> Burrs <input type="checkbox"/> Contamination <input type="checkbox"/> Countersink <input type="checkbox"/> Cut Too Short <input type="checkbox"/> Drill Holes <input type="checkbox"/> Drawing <input type="checkbox"/> Finish <input type="checkbox"/> Folio | | | <input type="checkbox"/> Grain <input type="checkbox"/> Hardware <input type="checkbox"/> Inspection Incomplete <input type="checkbox"/> Instructions Incomplete/Unclear <input type="checkbox"/> Maintenance <input type="checkbox"/> Mislabeled <input type="checkbox"/> Misread <input type="checkbox"/> Offset <input type="checkbox"/> Out of Calibration <input type="checkbox"/> Out of Sequence <input type="checkbox"/> Outside Dimensions | | | <input type="checkbox"/> Ovalized <input type="checkbox"/> Over/Under tolerance <input type="checkbox"/> Part Incorrect <input type="checkbox"/> Part Lost/Missing <input type="checkbox"/> Part Moved <input type="checkbox"/> Positioned Wrong <input type="checkbox"/> Power Loss/Surge | | <input type="checkbox"/> Pressure/Forced <input type="checkbox"/> Temperature/Cure <input type="checkbox"/> Weld <input type="checkbox"/> Wrong Stock Pulled <input type="checkbox"/> Other |

Picklist Print

November-27-12 10:47:41 AM

Page 3

Work Order ID: 93738

Parent Item: D350-748-201

Parent Item Name: Crosstube Installation, High Aft

Start Date: 11/22/12

Required Date: 12/21/12

Start Qty: 1.00

Required Qty: 1.00

D3500-1
Saddle

Manufactured No

220 Each 107.0000

Location Loc Qty Loc Code

ST423 27

85421 27

ST428A 72

86763 26

88346 22

89220 12

90055 12

ST429 8

90734 8

D3501-1
Bushing

Manufactured No

220 Each 215.0000

Location Loc Qty Loc Code

ST051 55

67757 4

73391 6

74866 45

ST053 160

86913 160

D3502-1
Support

Manufactured No

200 Each 93.0000

Location Loc Qty Loc Code

LG050 15

77041 15

ST051 10

73419 9

74873 1

ST053 68

86876 44

88465 24

November-27-12 10:47:42 AM

Shop Packet Print

Page 3

NCR: Yes / No

WORK ORDER NON-CONFORMANCE / UPDATE

DQA: _____ Date: _____

QA Closed: _____ Date: _____

| | | | | | | | | | | | | | | | | | | | | | | | | | | | |
|---|------------------------------------|--|---|---|----------------------|---|----------------|--------------|---|--|--|------------------------------------|------------------------------------|------------------------------------|--------------------------------------|------------------------------------|------------------------------------|--|----------------------------------|--|------------------------------------|--|--------------------------------|------------------------------------|------------------------------------|-----------------------------------|--|
| Work Order: _____ Part No. _____ NCR No. _____ | | | | DISPOSITION Rework <input type="checkbox"/> Scrap <input type="checkbox"/> Use-as-is <input type="checkbox"/> Work Order Update <input type="checkbox"/> | | AGAINST DEPARTMENT/PROCESS <table style="width: 100%; border: none;"> <tr> <td style="width: 25%;">Skid-tube <input type="checkbox"/></td> <td style="width: 25%;">Crosstube <input type="checkbox"/></td> <td style="width: 25%;">Water Jet <input type="checkbox"/></td> <td style="width: 25%;">Engineering <input type="checkbox"/></td> </tr> <tr> <td>Machining <input type="checkbox"/></td> <td>Small Fab <input type="checkbox"/></td> <td>Prod. Eng. Coord. <input type="checkbox"/></td> <td>Quality <input type="checkbox"/></td> </tr> <tr> <td>Thermoforming <input type="checkbox"/></td> <td>Finishing <input type="checkbox"/></td> <td>Rec/Store/Packaging <input type="checkbox"/></td> <td>Other <input type="checkbox"/></td> </tr> <tr> <td>Large Fab <input type="checkbox"/></td> <td>Composite <input type="checkbox"/></td> <td>Supplier <input type="checkbox"/></td> <td></td> </tr> </table> | | | | | | Skid-tube <input type="checkbox"/> | Crosstube <input type="checkbox"/> | Water Jet <input type="checkbox"/> | Engineering <input type="checkbox"/> | Machining <input type="checkbox"/> | Small Fab <input type="checkbox"/> | Prod. Eng. Coord. <input type="checkbox"/> | Quality <input type="checkbox"/> | Thermoforming <input type="checkbox"/> | Finishing <input type="checkbox"/> | Rec/Store/Packaging <input type="checkbox"/> | Other <input type="checkbox"/> | Large Fab <input type="checkbox"/> | Composite <input type="checkbox"/> | Supplier <input type="checkbox"/> | |
| Skid-tube <input type="checkbox"/> | Crosstube <input type="checkbox"/> | Water Jet <input type="checkbox"/> | Engineering <input type="checkbox"/> | | | | | | | | | | | | | | | | | | | | | | | | |
| Machining <input type="checkbox"/> | Small Fab <input type="checkbox"/> | Prod. Eng. Coord. <input type="checkbox"/> | Quality <input type="checkbox"/> | | | | | | | | | | | | | | | | | | | | | | | | |
| Thermoforming <input type="checkbox"/> | Finishing <input type="checkbox"/> | Rec/Store/Packaging <input type="checkbox"/> | Other <input type="checkbox"/> | | | | | | | | | | | | | | | | | | | | | | | | |
| Large Fab <input type="checkbox"/> | Composite <input type="checkbox"/> | Supplier <input type="checkbox"/> | | | | | | | | | | | | | | | | | | | | | | | | | |
| Root Cause | Date | Step | Qty | Description of work order update or Non-conformance | Initial Chief Eng | Action Description | Sign & Date | Verification | QC Inspector | | | | | | | | | | | | | | | | | | |
| Doc/Data <input type="checkbox"/> | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Equip/Tooling <input type="checkbox"/> | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Operator <input type="checkbox"/> | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Material <input type="checkbox"/> | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Setup <input type="checkbox"/> | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Other <input type="checkbox"/> | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Process <input type="checkbox"/> | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Supplier <input type="checkbox"/> | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Training <input type="checkbox"/> | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Unapproved <input type="checkbox"/> | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| FAULT CATEGORY | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Landing Gear <input type="checkbox"/> Bending <input type="checkbox"/> Centre Not Concentric to O/S <input type="checkbox"/> Cracks <input type="checkbox"/> Crushed/Crimped <input type="checkbox"/> Cuffs <input type="checkbox"/> Heat Treat <input type="checkbox"/> Inspection Strip in Tube <input type="checkbox"/> Ripples in Bend <input type="checkbox"/> Torque Waves in Extrusion <input type="checkbox"/> Turning Sequence <input type="checkbox"/> Wave/Twist in Tube | | | General <input type="checkbox"/> Bend <input type="checkbox"/> BOM/Route <input type="checkbox"/> Broken/Damaged <input type="checkbox"/> Burrs <input type="checkbox"/> Contamination <input type="checkbox"/> Countersink <input type="checkbox"/> Cut Too Short <input type="checkbox"/> Drill Holes <input type="checkbox"/> Drawing <input type="checkbox"/> Finish <input type="checkbox"/> Folio | | | <input type="checkbox"/> Grain <input type="checkbox"/> Hardware <input type="checkbox"/> Inspection Incomplete <input type="checkbox"/> Instructions Incomplete/Unclear <input type="checkbox"/> Maintenance <input type="checkbox"/> Mislabeled <input type="checkbox"/> Misread <input type="checkbox"/> Offset <input type="checkbox"/> Out of Calibration <input type="checkbox"/> Out of Sequence <input type="checkbox"/> Outside Dimensions | | | <input type="checkbox"/> Ovalized <input type="checkbox"/> Over/Under tolerance <input type="checkbox"/> Part Incorrect <input type="checkbox"/> Part Lost/Missing <input type="checkbox"/> Part Moved <input type="checkbox"/> Positioned Wrong <input type="checkbox"/> Power Loss/Surge _____ _____ _____ | | <input type="checkbox"/> Pressure/Forced <input type="checkbox"/> Temperature/Cure <input type="checkbox"/> Weld <input type="checkbox"/> Wrong Stock Pulled <input type="checkbox"/> Other _____ _____ _____ | | | | | | | | | | | | | | | | |

Picklist Print

November-27-12 10:47:42 AM

Page 4

Work Order ID: 93738

Parent Item: D350-748-201

Parent Item Name: Crosstube Installation, High Aft

Start Date: 11/22/12

Required Date: 12/21/12

Start Qty: 1.00

Required Qty: 1.00

D350-748-241TRN
Crosstube Turning Detail

Manufactured No

110 Each 3.0000

1

12-12-3

Location

Loc Qty

Loc Code

LG014

90672

3

79392

1

83287

1

86988

1

D3595-063-595

RUBBER CUSHION

Manufactured No

200 Each 66.0000

2

2

Location

Loc Qty

Loc Code

FG

5

87353

5

LG051

61

87353

61

MS2104214

Nut

Purchased No

220 Each 4,205.0000

24

8P 12-12-20.

Location

Loc Qty

Loc Code

314

184

122452

184

Return2012

8

123021

8

ST300

20

119017

20

ST314

3993

123021

1493

123248

900

123355

1600

November-27-12 10:47:42 AM

Shop Packet Print

Page 4

NCR: Yes / No

WORK ORDER NON-CONFORMANCE / UPDATE

DQA: _____ Date: _____

QA Closed: _____ Date: _____

| | | | | | | | | | | | | |
|---|------|------|---|---|-------------------|---|-------------|--------------|--|--|---|--|
| Work Order: _____ Part No. _____ NCR No. _____ | | | | DISPOSITION Rework <input type="checkbox"/> Scrap <input type="checkbox"/> Use-as-is <input type="checkbox"/> Work Order Update <input type="checkbox"/> | | AGAINST DEPARTMENT/PROCESS <div style="display: flex; justify-content: space-between;"> <div> Skid-tube <input type="checkbox"/> Machining <input type="checkbox"/> Thermoforming <input type="checkbox"/> Large Fab <input type="checkbox"/> </div> <div> Crosstube <input type="checkbox"/> Small Fab <input type="checkbox"/> Finishing <input type="checkbox"/> Composite <input type="checkbox"/> </div> <div> Water Jet <input type="checkbox"/> Prod. Eng. Coord. <input type="checkbox"/> Rec/Store/Packaging <input type="checkbox"/> Supplier <input type="checkbox"/> </div> <div> Engineering <input type="checkbox"/> Quality <input type="checkbox"/> Other <input type="checkbox"/> </div> </div> | | | | | | |
| Root Cause | Date | Step | Qty | Description of work order update or Non-conformance | Initial Chief Eng | Action Description | Sign & Date | Verification | QC Inspector | | | |
| Doc/Data <input type="checkbox"/> | | | | | | | | | | | | |
| Equip/Tooling <input type="checkbox"/> | | | | | | | | | | | | |
| Operator <input type="checkbox"/> | | | | | | | | | | | | |
| Material <input type="checkbox"/> | | | | | | | | | | | | |
| Setup <input type="checkbox"/> | | | | | | | | | | | | |
| Other <input type="checkbox"/> | | | | | | | | | | | | |
| Process <input type="checkbox"/> | | | | | | | | | | | | |
| Supplier <input type="checkbox"/> | | | | | | | | | | | | |
| Training <input type="checkbox"/> | | | | | | | | | | | | |
| Unapproved <input type="checkbox"/> | | | | | | | | | | | | |
| FAULT CATEGORY | | | | | | | | | | | | |
| Landing Gear <input type="checkbox"/> Bending <input type="checkbox"/> Centre Not Concentric to O/S <input type="checkbox"/> Cracks <input type="checkbox"/> Crushed/Crimped <input type="checkbox"/> Cuffs <input type="checkbox"/> Heat Treat <input type="checkbox"/> Inspection Strip in Tube <input type="checkbox"/> Ripples in Bend <input type="checkbox"/> Torque Waves in Extrusion <input type="checkbox"/> Turning Sequence <input type="checkbox"/> Wave/Twist in Tube | | | General <input type="checkbox"/> Bend <input type="checkbox"/> BOM/Route <input type="checkbox"/> Broken/Damaged <input type="checkbox"/> Burrs <input type="checkbox"/> Contamination <input type="checkbox"/> Countersink <input type="checkbox"/> Cut Too Short <input type="checkbox"/> Drill Holes <input type="checkbox"/> Drawing <input type="checkbox"/> Finish <input type="checkbox"/> Folio | | | <input type="checkbox"/> Grain <input type="checkbox"/> Hardware <input type="checkbox"/> Inspection Incomplete <input type="checkbox"/> Instructions Incomplete/Unclear <input type="checkbox"/> Maintenance <input type="checkbox"/> Mislabeled <input type="checkbox"/> Misread <input type="checkbox"/> Offset <input type="checkbox"/> Out of Calibration <input type="checkbox"/> Out of Sequence <input type="checkbox"/> Outside Dimensions | | | <input type="checkbox"/> Ovalized <input type="checkbox"/> Over/Under tolerance <input type="checkbox"/> Part Incorrect <input type="checkbox"/> Part Lost/Missing <input type="checkbox"/> Part Moved <input type="checkbox"/> Positioned Wrong <input type="checkbox"/> Power Loss/Surge | | <input type="checkbox"/> Pressure/Forced <input type="checkbox"/> Temperature/Cure <input type="checkbox"/> Weld <input type="checkbox"/> Wrong Stock Pulled <input type="checkbox"/> Other | |

Picklist Print

November-27-12 10:47:42 AM

Page 5

Work Order ID: 93738

Parent Item: D350-748-201

Parent Item Name: Crosstube Installation, High Aft

Start Date: 11/22/12

Required Date: 12/21/12

Start Qty: 1.00

Required Qty: 1.00

MS21042105

Purchased

No

220

Each

951.0000

4

4

SP

Num

Location

Loc Qty

Loc Code

300

29

121652

29

314

842

122452

842

ST300

80

108827

4

116105

1

116548

43

119109

20

2937

12

MS21920-22

Purchased

No

200

Each

68.0000

2

2

12-12-21

Clamp(per MIL-DTL-8783C)

Location

Loc Qty

Loc Code

LG050

68

116207

7

117506

1

118186

8

119545

1

120631

3

122838

48

November-27-12 10:47:42 AM

Shop Packet Print

Page 5

NCR: Yes / No

WORK ORDER NON-CONFORMANCE / UPDATE

DQA: _____ Date: _____

QA Closed: _____ Date: _____

| | | | | | | | | | | | | | | | | | | |
|--|---|---|--------------------------------------|------------------------------------|------------------------------------|--------------------------------------|------------------------------------|------------------------------------|--|----------------------------------|--|------------------------------------|--|--------------------------------|------------------------------------|------------------------------------|-----------------------------------|--|
| Work Order: _____ Part No. _____ NCR No. _____ | DISPOSITION Rework <input type="checkbox"/> Scrap <input type="checkbox"/> Use-as-is <input type="checkbox"/> Work Order Update <input type="checkbox"/> | AGAINST DEPARTMENT/PROCESS <table style="width: 100%;"> <tr> <td>Skid-tube <input type="checkbox"/></td> <td>Crosstube <input type="checkbox"/></td> <td>Water Jet <input type="checkbox"/></td> <td>Engineering <input type="checkbox"/></td> </tr> <tr> <td>Machining <input type="checkbox"/></td> <td>Small Fab <input type="checkbox"/></td> <td>Prod. Eng. Coord. <input type="checkbox"/></td> <td>Quality <input type="checkbox"/></td> </tr> <tr> <td>Thermoforming <input type="checkbox"/></td> <td>Finishing <input type="checkbox"/></td> <td>Rec/Store/Packaging <input type="checkbox"/></td> <td>Other <input type="checkbox"/></td> </tr> <tr> <td>Large Fab <input type="checkbox"/></td> <td>Composite <input type="checkbox"/></td> <td>Supplier <input type="checkbox"/></td> <td></td> </tr> </table> | Skid-tube <input type="checkbox"/> | Crosstube <input type="checkbox"/> | Water Jet <input type="checkbox"/> | Engineering <input type="checkbox"/> | Machining <input type="checkbox"/> | Small Fab <input type="checkbox"/> | Prod. Eng. Coord. <input type="checkbox"/> | Quality <input type="checkbox"/> | Thermoforming <input type="checkbox"/> | Finishing <input type="checkbox"/> | Rec/Store/Packaging <input type="checkbox"/> | Other <input type="checkbox"/> | Large Fab <input type="checkbox"/> | Composite <input type="checkbox"/> | Supplier <input type="checkbox"/> | |
| Skid-tube <input type="checkbox"/> | Crosstube <input type="checkbox"/> | Water Jet <input type="checkbox"/> | Engineering <input type="checkbox"/> | | | | | | | | | | | | | | | |
| Machining <input type="checkbox"/> | Small Fab <input type="checkbox"/> | Prod. Eng. Coord. <input type="checkbox"/> | Quality <input type="checkbox"/> | | | | | | | | | | | | | | | |
| Thermoforming <input type="checkbox"/> | Finishing <input type="checkbox"/> | Rec/Store/Packaging <input type="checkbox"/> | Other <input type="checkbox"/> | | | | | | | | | | | | | | | |
| Large Fab <input type="checkbox"/> | Composite <input type="checkbox"/> | Supplier <input type="checkbox"/> | | | | | | | | | | | | | | | | |

| Root Cause | Date | Step | Qty | Description of work order update or Non-conformance | Initial Chief Eng | Action Description | Sign & Date | Verification | QC Inspector |
|---------------|------|------|-----|---|-------------------|--------------------|-------------|--------------|--------------|
| Doc/Data | | | | | | | | | |
| Equip/Tooling | | | | | | | | | |
| Operator | | | | | | | | | |
| Material | | | | | | | | | |
| Setup | | | | | | | | | |
| Other | | | | | | | | | |
| Process | | | | | | | | | |
| Supplier | | | | | | | | | |
| Training | | | | | | | | | |
| Unapproved | | | | | | | | | |

FAULT CATEGORY

| Landing Gear | General | Other |
|---|---|--|
| <input type="checkbox"/> Bending | <input type="checkbox"/> Bend | <input type="checkbox"/> Grain |
| <input type="checkbox"/> Centre Not Concentric to O/S | <input type="checkbox"/> BOM/Route | <input type="checkbox"/> Hardware |
| <input type="checkbox"/> Cracks | <input type="checkbox"/> Broken/Damaged | <input type="checkbox"/> Inspection Incomplete |
| <input type="checkbox"/> Crushed/Crimped | <input type="checkbox"/> Burrs | <input type="checkbox"/> Instructions Incomplete/Unclear |
| <input type="checkbox"/> Cuffs | <input type="checkbox"/> Contamination | <input type="checkbox"/> Maintenance |
| <input type="checkbox"/> Heat Treat | <input type="checkbox"/> Countersink | <input type="checkbox"/> Mislabeled |
| <input type="checkbox"/> Inspection Strip in Tube | <input type="checkbox"/> Cut Too Short | <input type="checkbox"/> Misread |
| <input type="checkbox"/> Ripples in Bend | <input type="checkbox"/> Drill Holes | <input type="checkbox"/> Offset |
| <input type="checkbox"/> Torque Waves in Extrusion | <input type="checkbox"/> Drawing | <input type="checkbox"/> Out of Calibration |
| <input type="checkbox"/> Turning Sequence | <input type="checkbox"/> Finish | <input type="checkbox"/> Out of Sequence |
| <input type="checkbox"/> Wave/Twist in Tube | <input type="checkbox"/> Folio | <input type="checkbox"/> Outside Dimensions |
| | | <input type="checkbox"/> Ovalized |
| | | <input type="checkbox"/> Over/Under tolerance |
| | | <input type="checkbox"/> Part Incorrect |
| | | <input type="checkbox"/> Part Lost/Missing |
| | | <input type="checkbox"/> Part Moved |
| | | <input type="checkbox"/> Positioned Wrong |
| | | <input type="checkbox"/> Power Loss/Surge |
| | | <input type="checkbox"/> Pressure/Forced |
| | | <input type="checkbox"/> Temperature/Cure |
| | | <input type="checkbox"/> Weld |
| | | <input type="checkbox"/> Wrong Stock Pulled |
| | | <input type="checkbox"/> Other |

Picklist Print

November-27-12 10:47:42 AM

Page 6

Work Order ID: 93738

Parent Item: D350-748-201

Parent Item Name: Crosstube Installation, High Aft

Start Date: 11/22/12

Required Date: 12/21/12

Start Qty: 1.00

Required Qty: 1.00

MS27039-1-10

Purchased

No

200

Each

706.0000

1

Screw

~~89352~~
At 12-12-21

Location

Loc Qty

Loc Code

GA

100

120449

100

ST291

5

120120

5

ST305

598

122815

300

123522

298

ST308

3

122027

3

① ~~12~~

D2856-400

Abrasion Strip

89352

①

At 12-12-21

NCR: Yes / No

WORK ORDER NON-CONFORMANCE / UPDATE


DQA: _____ Date: _____

QA Closed: _____ Date: _____

| | | | | | | | | | | | | | | | | | | | | | | | | | | | |
|--|------------------------------------|--|---|---|-------------------|---|-------------|--------------|--|--|---|------------------------------------|------------------------------------|------------------------------------|--------------------------------------|------------------------------------|------------------------------------|--|----------------------------------|--|------------------------------------|--|--------------------------------|------------------------------------|------------------------------------|-----------------------------------|--|
| Work Order: _____ Part No. _____ NCR No. _____ | | | | DISPOSITION Rework <input type="checkbox"/> Scrap <input type="checkbox"/> Use-as-is <input type="checkbox"/> Work Order Update <input type="checkbox"/> | | AGAINST DEPARTMENT/PROCESS <table style="width: 100%; border: none;"> <tr> <td style="width: 25%;">Skid-tube <input type="checkbox"/></td> <td style="width: 25%;">Crosstube <input type="checkbox"/></td> <td style="width: 25%;">Water Jet <input type="checkbox"/></td> <td style="width: 25%;">Engineering <input type="checkbox"/></td> </tr> <tr> <td>Machining <input type="checkbox"/></td> <td>Small Fab <input type="checkbox"/></td> <td>Prod. Eng. Coord. <input type="checkbox"/></td> <td>Quality <input type="checkbox"/></td> </tr> <tr> <td>Thermoforming <input type="checkbox"/></td> <td>Finishing <input type="checkbox"/></td> <td>Rec/Store/Packaging <input type="checkbox"/></td> <td>Other <input type="checkbox"/></td> </tr> <tr> <td>Large Fab <input type="checkbox"/></td> <td>Composite <input type="checkbox"/></td> <td>Supplier <input type="checkbox"/></td> <td></td> </tr> </table> | | | | | | Skid-tube <input type="checkbox"/> | Crosstube <input type="checkbox"/> | Water Jet <input type="checkbox"/> | Engineering <input type="checkbox"/> | Machining <input type="checkbox"/> | Small Fab <input type="checkbox"/> | Prod. Eng. Coord. <input type="checkbox"/> | Quality <input type="checkbox"/> | Thermoforming <input type="checkbox"/> | Finishing <input type="checkbox"/> | Rec/Store/Packaging <input type="checkbox"/> | Other <input type="checkbox"/> | Large Fab <input type="checkbox"/> | Composite <input type="checkbox"/> | Supplier <input type="checkbox"/> | |
| Skid-tube <input type="checkbox"/> | Crosstube <input type="checkbox"/> | Water Jet <input type="checkbox"/> | Engineering <input type="checkbox"/> | | | | | | | | | | | | | | | | | | | | | | | | |
| Machining <input type="checkbox"/> | Small Fab <input type="checkbox"/> | Prod. Eng. Coord. <input type="checkbox"/> | Quality <input type="checkbox"/> | | | | | | | | | | | | | | | | | | | | | | | | |
| Thermoforming <input type="checkbox"/> | Finishing <input type="checkbox"/> | Rec/Store/Packaging <input type="checkbox"/> | Other <input type="checkbox"/> | | | | | | | | | | | | | | | | | | | | | | | | |
| Large Fab <input type="checkbox"/> | Composite <input type="checkbox"/> | Supplier <input type="checkbox"/> | | | | | | | | | | | | | | | | | | | | | | | | | |
| Root Cause | Date | Step | Qty | Description of work order update or Non-conformance | Initial Chief Eng | Action Description | Sign & Date | Verification | QC Inspector | | | | | | | | | | | | | | | | | | |
| Doc/Data <input type="checkbox"/> | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Equip/Tooling <input type="checkbox"/> | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Operator <input type="checkbox"/> | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Material <input type="checkbox"/> | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Setup <input type="checkbox"/> | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Other <input type="checkbox"/> | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Process <input type="checkbox"/> | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Supplier <input type="checkbox"/> | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Training <input type="checkbox"/> | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Unapproved <input type="checkbox"/> | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| FAULT CATEGORY | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Landing Gear <input type="checkbox"/> Bending <input type="checkbox"/> Centre Not Concentric to O/S <input type="checkbox"/> Cracks <input type="checkbox"/> Crushed/Crimped. <input type="checkbox"/> Cuffs <input type="checkbox"/> Heat Treat <input type="checkbox"/> Inspection Strip in Tube <input type="checkbox"/> Ripples in Bend <input type="checkbox"/> Torque Waves in Extrusion <input type="checkbox"/> Turning Sequence <input type="checkbox"/> Wave/Twist in Tube | | | General <input type="checkbox"/> Bend <input type="checkbox"/> BOM/Route <input type="checkbox"/> Broken/Damaged <input type="checkbox"/> Burrs <input type="checkbox"/> Contamination <input type="checkbox"/> Countersink <input type="checkbox"/> Cut Too Short <input type="checkbox"/> Drill Holes <input type="checkbox"/> Drawing <input type="checkbox"/> Finish <input type="checkbox"/> Folio | | | <input type="checkbox"/> Grain <input type="checkbox"/> Hardware <input type="checkbox"/> Inspection Incomplete <input type="checkbox"/> Instructions Incomplete/Unclear <input type="checkbox"/> Maintenance <input type="checkbox"/> Mislabeled <input type="checkbox"/> Misread <input type="checkbox"/> Offset <input type="checkbox"/> Out of Calibration <input type="checkbox"/> Out of Sequence <input type="checkbox"/> Outside Dimensions | | | <input type="checkbox"/> Ovalized <input type="checkbox"/> Over/Under tolerance <input type="checkbox"/> Part Incorrect <input type="checkbox"/> Part Lost/Missing <input type="checkbox"/> Part Moved <input type="checkbox"/> Positioned Wrong <input type="checkbox"/> Power Loss/Surge | | <input type="checkbox"/> Pressure/Forced <input type="checkbox"/> Temperature/Cure <input type="checkbox"/> Weld <input type="checkbox"/> Wrong Stock Pulled <input type="checkbox"/> Other | | | | | | | | | | | | | | | | |

| | | | |
|--|-----------------------|---------------------|--------------|
| DART AEROSPACE LTD | | Work Order: | 93738 |
| Description: Crosstube High Aft (AS350/355) | | Part Number: | D350-748-201 |
| Inspection Dwg: D350-748-241 | Rev: <i>FL</i> | Page 1 of 1 | |

| Required Dimension | Min | Max |
|--------------------|-------|-------|
| Height | 31.22 | 31.48 |
| 1/2 Span | 40.77 | 41.03 |
| Angle | 75 | 77 |
| Total Span | 81.54 | 82.06 |
| Bending Passes | 7 | -- |
| Crushing | -- | 6% |
| Twist | -- | 0.25 |

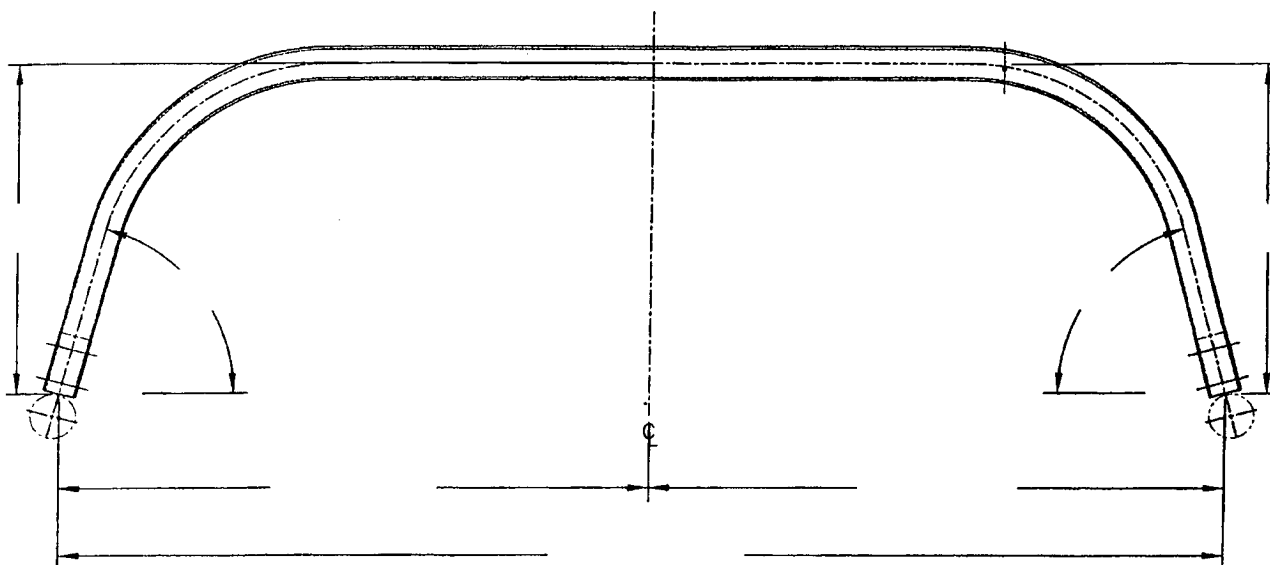

| | Side A | Side B |
|----------------|--------|--------|
| Bending Passes | | |
| Crushing | | |
| Comments | | |
| | | |
| | | |
| | | |
| | | |

| | |
|-----------------|--|
| QC15 Inspection | |
| Date | |

| Rev | Date | Change | Revised by | Approved |
|-----|----------|--|------------|----------|
| A | 07.02.06 | New Issue | KJ/JM | |
| B | 10.08.23 | Dwg Rev updated | KJ | |
| C | 12.04.16 | Added bending, crushing & twist dimensions | KJ | |
| D | 12.07.31 | Dwg Rev updated | KJ | |

| Item | Qty -241 | Part Number | Description |
|------|-------------|-----------------------------|---|
| 1 | X | D350-748-241 | CROSSTUBE ASSEMBLY (AS 350/355 HI AFT) |
| 2 | 1 | D6015-125 | CROSSTUBE (OR D6018-125) |
| 3 | 2 | D3502-1 | SUPPORT |
| 4 | 2 | D3595-063-395 | RUBBER CUSHION |
| 5 | 1 | AELS-1032-225 | INSERT |
| 6 | 1 | NAS1149D0363J | WASHER (OR AN960JD10) |
| 7 | 2 | MS21920-22 OR MS21920-21 | CLAMP (PER DART SPEC. M-MS21920-21/-22) |
| 8 | 1 | MS27039-1-10 | SCREW |
| 9 | A/R | PROSEAL 890 B-2 | SEALANT, AMS-S-8802 CLASS B-2 |

GENERAL NOTES:

- 1) MATERIAL: MANUFACTURED FROM D6015-125 OR D6018-125
FINISHED LENGTH AFTER TURNING = 124.70±0.06 (AFTER BENDING/TRIMMING = 122.70 REF)
- 2) FINISH: MAGNETIC PARTICLE INSPECT PER DART QSI 038 4.2
CADIUM PLATE PER AMS-QQ-P-416B, CLASS 1, TYPE II
PRIME INSIDE AND OUTSIDE PER DART QSI 005 4.2
PAINT OUTSIDE PER DART QSI 005 4.2
- 3) TOLERANCE: PER DART QSI 018 UNLESS OTHERWISE NOTED.
WALL THICKNESS ECCENTRICITY PER DART QSI 038 7.2
MIN. ALLOWABLE WALL IS -0.020 FROM NOMINAL
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED.
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX.
- 6) IDENTIFICATION: DART PART NUMBER "D350-748-241" AND BATCH NUMBER ON INSIDE OF CUFF
PER DART QSI 044 6.4 (VIBRATING STYLUS)
- 7) WEIGHT: 29.85 lbs
- 8) PART IS SYMMETRIC ABOUT CENTERLINE, EXCEPT FOR Ø0.297 HOLE.
- 9) EXTREME CARE MUST BE TAKEN TO PROTECT THE OUTSIDE SURFACE OF THE TUBE. THE OUTSIDE SURFACE MUST BE SMOOTH AND FREE FROM SURFACE DEFECTS SUCH AS SCRATCHES, NICKS, OR DENTS. DEFECTS UP TO 0.005" MAY BE BLENDED OUT LONGITUDINALLY. CIRCUMFERENTIAL GRIND MARKS ARE UNACCEPTABLE. WHEN DRILLING HOLES EXTREME CARE MUST BE TAKEN AND CAREFUL DEBURRING PERFORMED TO ENSURE A CLEAN HOLE WITH NO CRACKING/CHIPPING/GROOVES.

TURNING

- 10) BLEND OUT ALL EDGES FROM MACHINING LONGITUDINALLY. TRANSITION SHOULD BE SMOOTH. NOTE: ALL HOLES ARE DRILLED AFTER BENDING.
- 11) HEAT TREAT TO MIN. 180 KSI PER MIL-T-6736 OR AMS2759/1E AFTER TURNING. ACCEPTABLE TO VERIFY TENSILE STRENGTH BY HARDNESS TEST PER ASTM E18 TO 40-45 HRC.

BENDING

- 12) ALL DIMENSIONS FOR BENT TUBE ARE POST STRESS RELIEF
- 13) BEND PROGRESSIVELY WITH A MINIMUM OF 7 PASSES PER SIDE. MAXIMUM TUBE FLATTENING DUE TO BENDING IS 6% BASED ON O.D. ON TOP HALF OF BEND, AND 7% ON BOTTOM HALF OF BEND.
- 14) MAX AMPLITUDE OF RIBBLING ALONG BENT PORTION OF THE TUBE IS 0.030 (ZN A1-3)
- 15) AFTER BENDING, STRESS RELIEVE TUBE AT 650°F ±0.25°F FOR A MINIMUM OF 2 HRS AND ALLOW TO COOL TO AMBIENT TEMPERATURE (REF AMS2759/1E).
- 16) MAX TWIST AFTER STRESS RELIEF: WITH XTUBE LAYED FLAT ON SURFACE, THE DIFFERENCE BETWEEN CUFF HEIGHTS FROM THE SURFACE MAY BE NO LARGER THAN 0.38 (ZN C1-3).

ASSEMBLY

- 17) TO INSTALL D3502-1 SUPPORT: ABRABE MATING SURFACE OF SUPPORT AND CROSSTUBE WITH 180-GRIT SANDPAPER AND REMOVE RESIDUE WITH MEK (OR EQUIVALENT). APPLY A 0.02" TO 0.05" THICK LAYER OF PROSEAL 890 CLASS B-2 (OR AMS-S-8802 CLASS B-2) SEALANT TO MATING SURFACE OF SUPPORT.
- 18) TORQUE CLAMPS 60 TO 80 IN-LB. ENSURE AT LEAST 1.5 THREADS SHOWING IN SAFETY AND THAT NUT HAS NOT BOTTOMED-OUT AFTER TORQUING. PRIOR TO PACKAGING, RE-CHECK TORQUE ON CLAMPS AFTER PROSEAL 890 SEALANT HAS CURED FOR 72 HOURS.

SHIP COPY
RETURN TO
ENGINEERING
UNCONTROLLED COPY
SUBMIT TO MANAGEMENT

WORK IN PROGRESS
WORK IN PROGRESS


93738 MLJ

12-11-27


RELEASE
2012-11-01

| | | | |
|---|--|----|----------|
| G | RMV ABRASION STRIP, SUPPORT NOW W/ PROSEAL & CUSHION, ADD STRESS RELIEF, LONGER CUFF, NOW TRIM/D AFTER BEND, ADD WALL DIMS & UPDATE TOL. | CP | 12.09.12 |
| F | ADD HRC TEST OPTION (B8-1) PER PAR 09-040, ADD TWIST LIMIT (A8-1, C1-3), ADD D6015-125 OPTION (C8-1), STOCK DIM NOW MACHINED (D1-4) | CP | 10.11.23 |
| E | REVISE GENERAL NOTES; UPDATE TO CURRENT STANDARDS; RELOCATED FLAG #6 PER PAR 08-046 (ZN A8-3); ADD TOLERANCES (ZN C6-3, D2-3) | RF | 09.09.30 |
| D | MAG. PARTICLE AND CAD PLATE AS MFD. | CP | 06.10.31 |
| C | ADD CAD PLATING | CP | 06.08.14 |
| B | ADD D6018-125 & PRIME AND PAINT | CP | 06.06.30 |
| A | NEW ISSUE | CP | 06.03.31 |
| REV. | DESCRIPTION | BY | DATE |
| DESIGN | | | |
| DRAWN | | | |
| CHECKED | | | |
| MFG. APPR. | | | |
| APPROVED | | | |
| DE APPR. | | | |
| DATE | 12.09.12 | | |
| DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA DRAWING NO. D350-748-241 REV. G SHEET 1 OF 4 TITLE CROSSTUBE (AS 350/355 HI AFT) NTS SCALE COPYRIGHT © 2005 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD. | | | |

93738

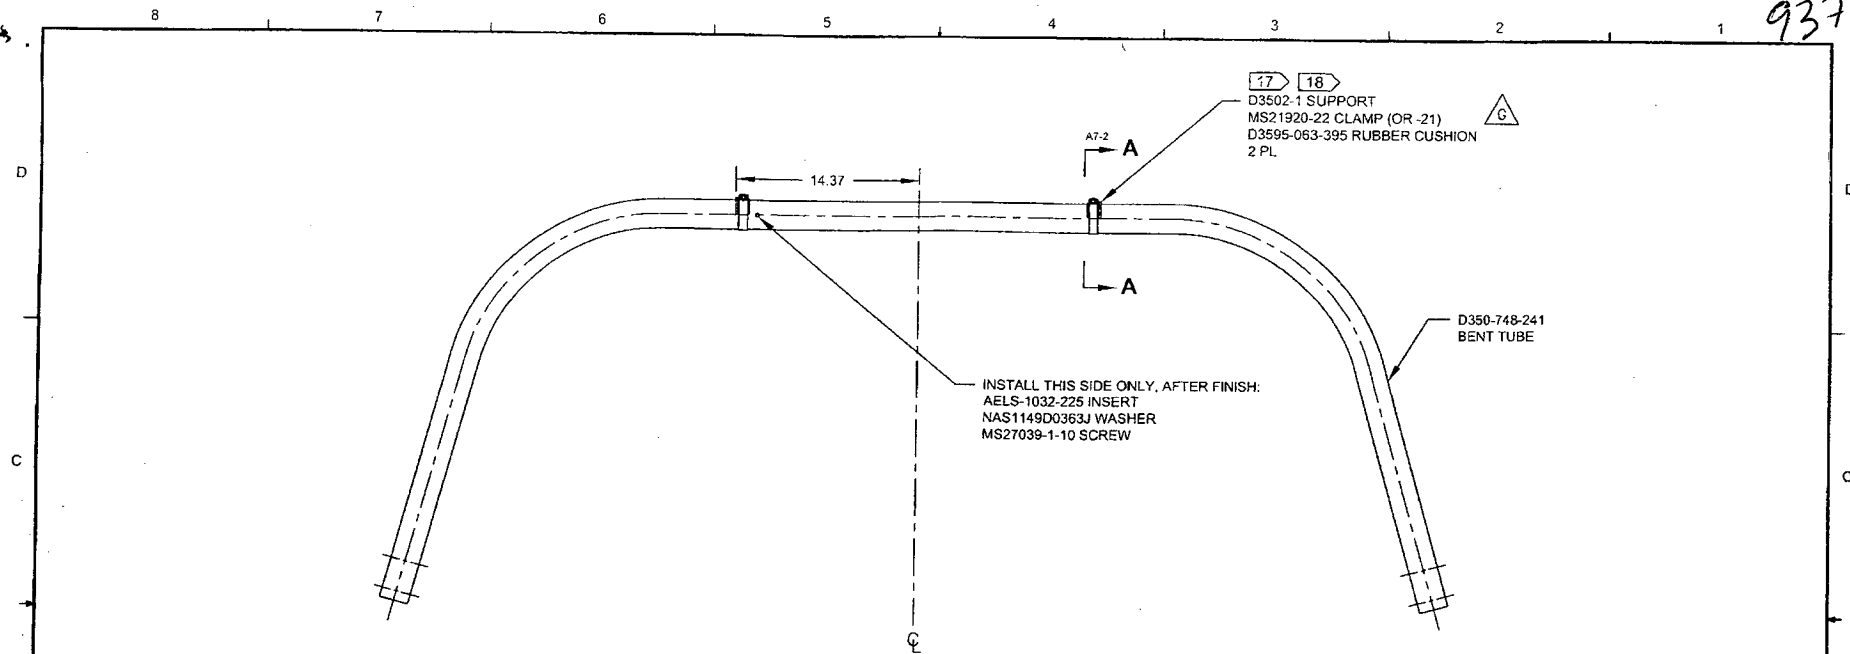

**D350-748-241
ASSEMBLY DETAIL**


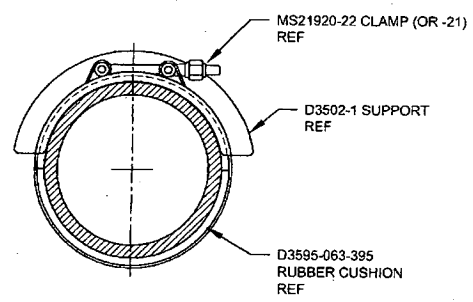


SECTION A-A D4-2
SCALE 6X



RELEASED
2012-11-01

| | | | |
|------------|----------|--|--------------|
| DESIGN | 90 | DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA | |
| DRAWN | 90 | | |
| CHECKED | AS | DRAWING NO. | REV. G |
| MFG. APPR. | AS | D350-748-241 | SHEET 2 OF 4 |
| APPROVED | AS | TITLE | SCALE |
| DE APPR. | AS | CROSSTUBE (AS 350/355 HI AFT) | NTS |
| DATE | 12.09.12 | <small>COPYRIGHT © 2006 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR LOANED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.</small> | |

93738

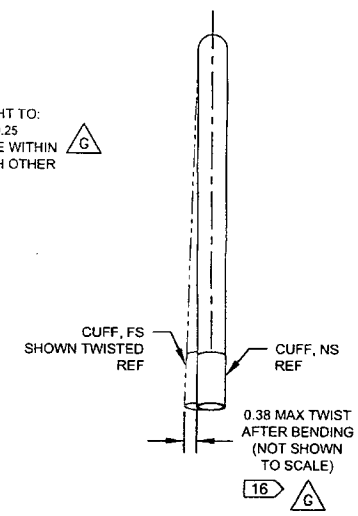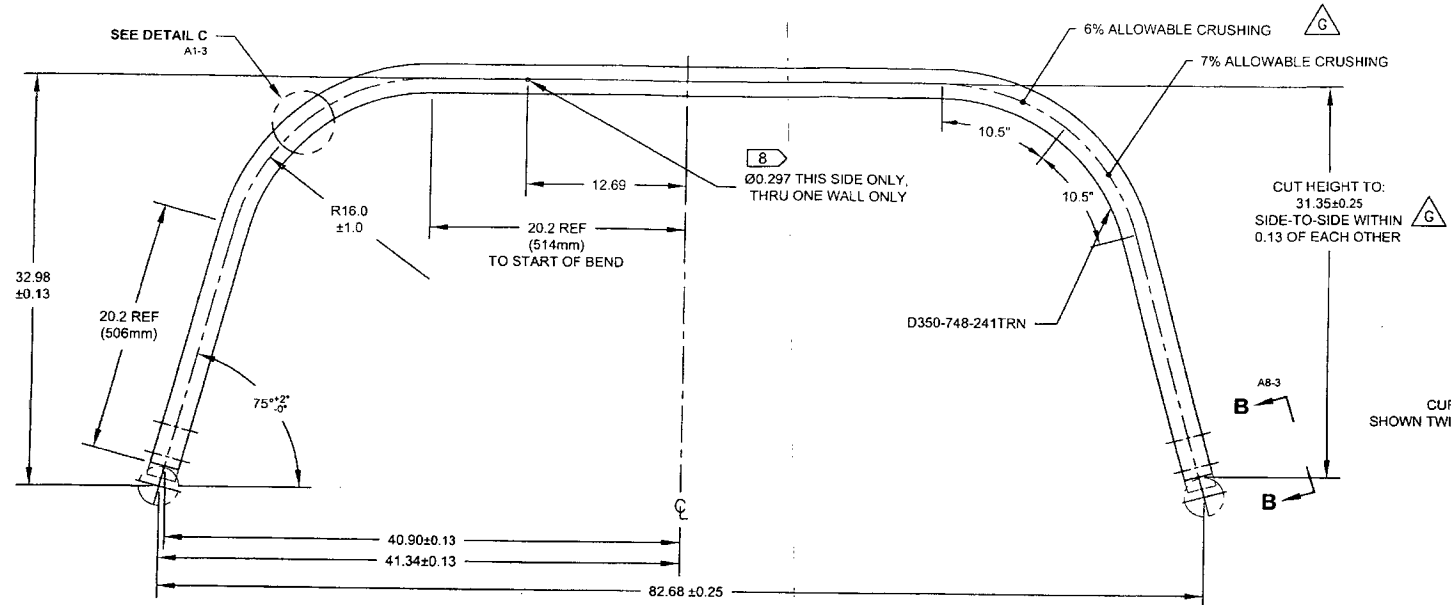


**D350-748-241
BENDING AND DRILLING DETAIL**

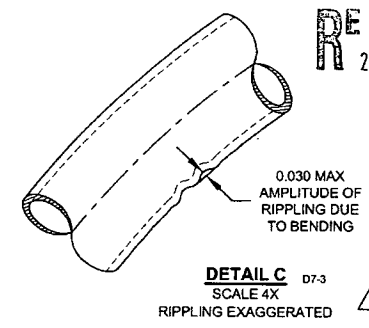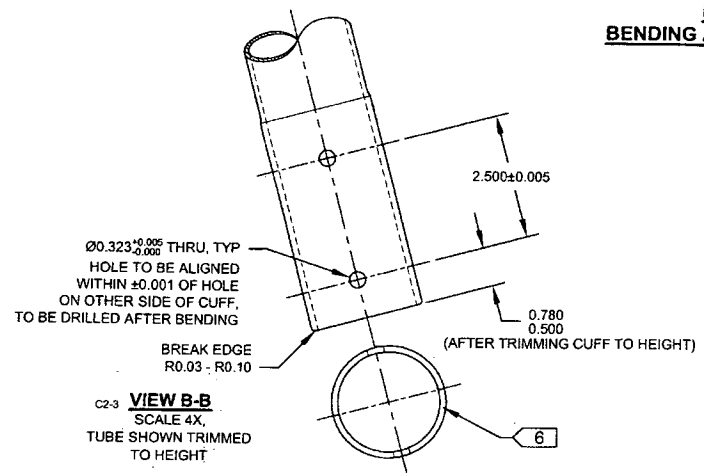

| | | | |
|------------|----------|--|--------------|
| DESIGN | D | DART AEROSPACE LTD | |
| DRAWN | D | HAWKESBURY, ONTARIO, CANADA | |
| CHECKED | A.P. | DRAWING NO. | REV. G |
| MFG. APPR. | | D350-748-241 | SHEET 3 OF 4 |
| APPROVED | | TITLE | SCALE |
| DE APPR. | | CROSSTUBE (AS 350/355 HI AFT) | NTS |
| DATE | 12.09.12 | <small>COPYRIGHT © 2006 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COMMERCE TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.</small> | |

93738

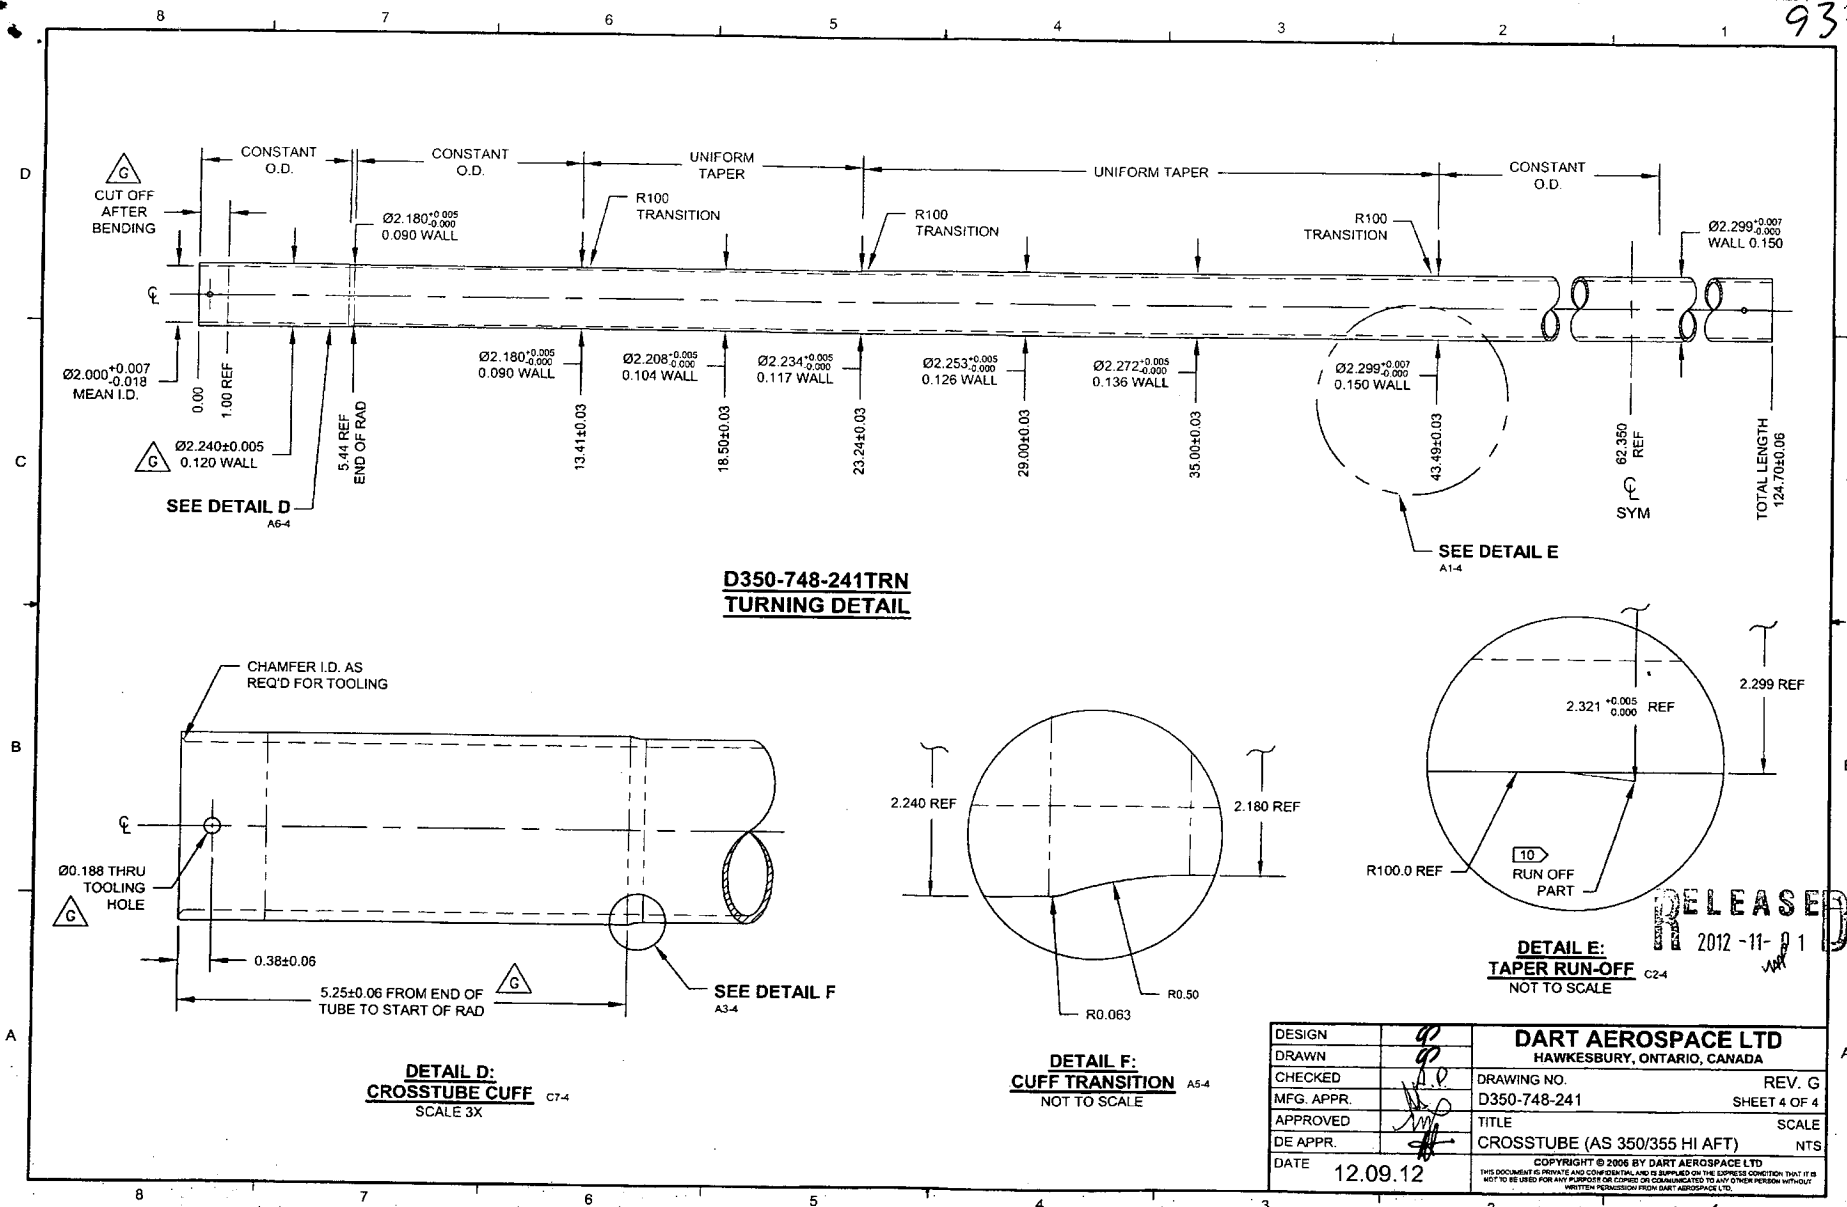

**D350-748-241TRN
TURNING DETAIL**

**DETAIL D:
CROSSTUBE CUFF** C7.4
SCALE 3X

**DETAIL F:
CUFF TRANSITION** A5.4
NOT TO SCALE

**DETAIL E:
TAPER RUN-OFF** C2.4
NOT TO SCALE


| | | | |
|------------|----------|--|--------------|
| DESIGN | 92 | DART AEROSPACE LTD | |
| DRAWN | 92 | HAWKESBURY, ONTARIO, CANADA | |
| CHECKED | 92 | DRAWING NO. | REV. G |
| MFG. APPR. | 92 | D350-748-241 | SHEET 4 OF 4 |
| APPROVED | 92 | TITLE | SCALE |
| DE APPR. | 92 | CROSSTUBE (AS 350/355 HI AFT) | NTS |
| DATE | 12.09.12 | <small>COPYRIGHT © 2006 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.</small> | |

RELEASED
2012-11-01

Measured Before De-Stress

| | |
|---|---------------------------|
| DART AEROSPACE LTD | Work Order: 93988 |
| Description: Crosstube High Aft (AS350/355) | Part Number: D350-748-201 |
| Inspection Dwg: D350-748-241 Rev: F | Page 1 of 1 |

| Required Dimension | Min | Max |
|--------------------|-------|-------|
| Height | 31.22 | 31.48 |
| 1/2 Span | 40.77 | 41.03 |
| Angle | 75 | 77 |
| Total Span | 81.54 | 82.06 |
| Bending Passes | 7 | -- |
| Crushing | -- | 6% |
| Twist | -- | 0.25 |

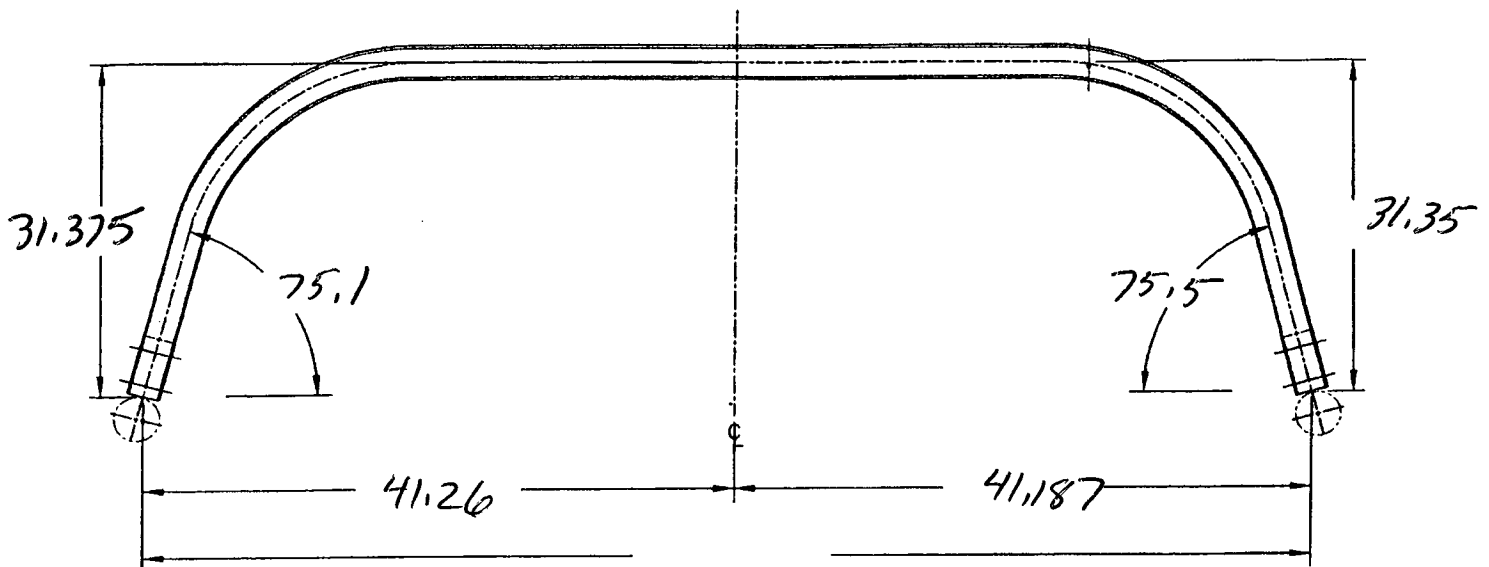

| | Side A | Side B |
|----------------|--------|--------|
| Bending Passes | 38 | 38 |
| Crushing | | |
| Comments | | |
| TWIST 0.060 | | |
| | | |
| | | |
| | | |

12-12-3


| | |
|-----------------|--|
| QC15 Inspection | |
| Date | |

| Rev | Date | Change | Revised by | Approved |
|-----|----------|--|------------|----------|
| A | 07.02.06 | New Issue | KJ/JM | |
| B | 10.08.23 | Dwg Rev updated | KJ | |
| C | 12.04.16 | Added bending, crushing & twist dimensions | KJ | |
| D | 12.07.31 | Dwg Rev updated | KJ | |



| | | | |
|--|--|---------------------|--------------------|
| DART AEROSPACE LTD | | Work Order: | 93738 |
| Description: Crosstube High Aft (AS350/355) | | Part Number: | D350-748-201 |
| Inspection Dwg: D350-748-241 | | Rev: F | Page 1 of 1 |

| Required Dimension | Min | Max |
|--------------------|-------|-------|
| Height | 31.22 | 31.48 |
| 1/2 Span | 40.77 | 41.03 |
| Angle | 75 | 77 |
| Total Span | 81.54 | 82.06 |
| Bending Passes | 7 | -- |
| Crushing | -- | 6% |
| Twist | -- | 0.25 |

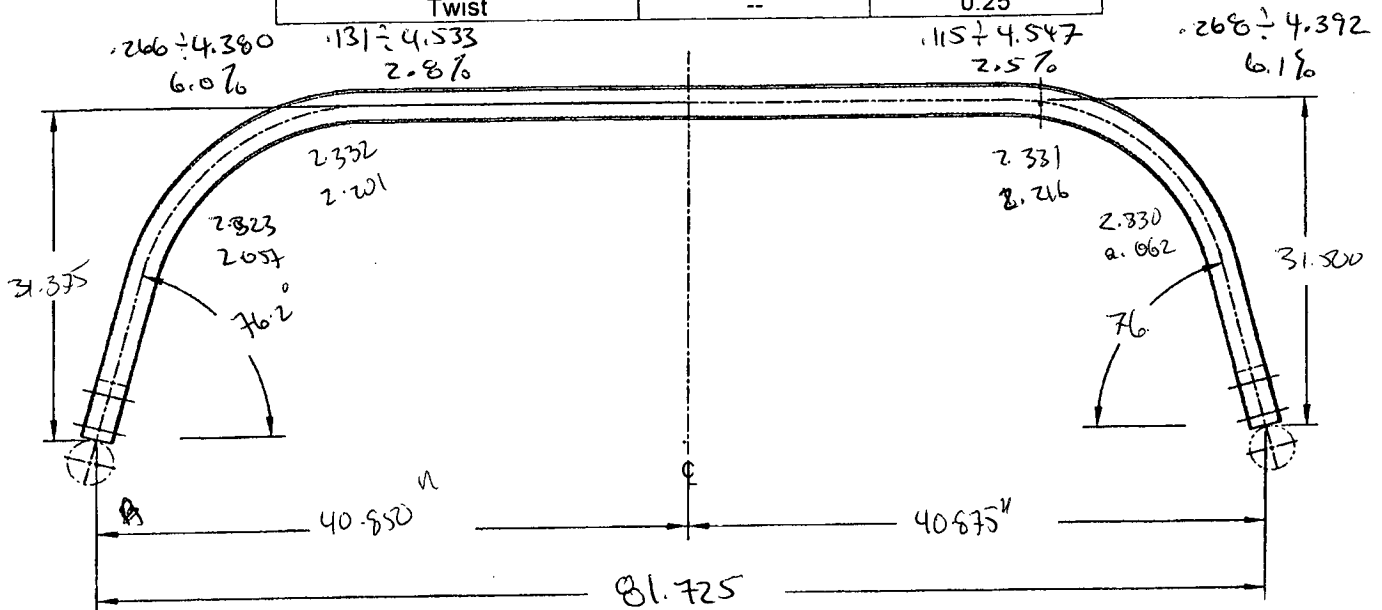

| | Side A | Side B |
|----------------|------------------|------------------------|
| Bending Passes | | |
| Crushing | | |
| Comments | | |
| Twist = 0.115" | | |
| Side A | Top = 2.8% crush | Bottom = 6.0% crushing |
| Side B | Top = 2.5% crush | Bottom = 6.1% crushing |

Acceptable to
Rev. G of
dwg
12.12.06

| | |
|-----------------|------------------|
| QC15 Inspection | DAS 16 |
| Date | 12/12/07 |

| Rev | Date | Change | Revised by | Approved |
|-----|----------|--|------------|----------|
| A | 07.02.06 | New Issue | KJ/JM | |
| B | 10.08.23 | Dwg Rev updated | KJ | |
| C | 12.04.16 | Added bending, crushing & twist dimensions | KJ | |
| D | 12.07.31 | Dwg Rev updated | KJ | |



Metcor Inc.

560, boul. Arthur-Sauvé, St-Eustache (Québec) J7R 5A8
Tél. 450 473-1884
Télécopieur/Fax administration 450 491-5498
Télécopieur/Fax production 450 491-6454

Page 1 / 1

Certificat de Conformité Certificate of Compliance

| BON DE TRAVAIL order | CHARGEMENT load |
|-------------------------|--------------------|
| 181760 | 1 |

CLIENT / customer 215

DART AEROSPACE
1270 ABERDEEN
HAWKESBURY

ON K6A 1K7

LIVRÉ À / shipped to:

DART AEROSPACE
1270 ABERDEEN
HAWKESBURY

ON K6A 1K7

| COMMANDE DU CLIENT customer po | BON DE LIVRAISON DU CLIENT customer shipper no. | MATÉRIEL material | CODE DE TRAITEMENT mat'l heat code | NUMÉRO DE LOT lot number |
|---|--|--|---------------------------------------|-----------------------------|
| PO8563 | | Steel | | |
| SPECIFICATIONS DU PROCÉDÉ processing specifications | | | | |
| STRESS REL | | | | |
| SAE AMS 2759/1 REV.E | | | | |
| EXIGENCE / requirement SPECIFICATIONS / specified TESTS EXÉCUTÉS / performed RÉSULTATS DE TESTS / results | | | | |
| Visual | | | | |
| QUANTITÉ quantity | POIDS weight | DESCRIPTION DES PIÈCES parts description | | |
| 5 | 150 | D350-748-101 (1) CROSSTUBE REFERENCE: 93257 (1) D350-748-101 CROSSTUBE REFERENCE: 85565 (1) D350-748-201 CROSSTUBE REFERENCE 92143 (1) D3350-748-201 CROSSTUBE REFERENCE: 89992 (1) D350-748-201 CROSSTUBE REFERENCE 93739 CONTENANT: 1 NIL | | |

COMMENTAIRES / comments

METCOR INC.

560 BOUL. ARTHUR-SAUVÉ

ST-EUSTACHE, QC, J7R 5A8

Tel: 450-473-1884 / Fax: 450-491-5498

Certificat de Conformité Détaillé

Detailed Certificate of Compliance

| BON DE TRAVAIL order | CHARGEMENT load |
|-------------------------|--------------------|
| 181760 | 1 |

CLIENT / customer 215

DART AEROSPACE

1270 ABERDEEN

HAWKESBURY

ON K6A 1K7

LIVRÉ À / shipped to:

DART AEROSPACE

1270 ABERDEEN

HAWKESBURY

ON K6A 1K7

1

| Operation | Temp. spécifiée Specified Temp | Temps de trempe Spécifié Specified Soak Temp | Atmosphere | Carbone Carbon Potential | Q-Media Q-Temp | Four # Furnace # | Date Départ Start Date | Heure d'entrée Time In | Heure de sortie Time Out | Date Complétée Date complete |
|--------------------|-----------------------------------|---|------------|--------------------------------|-------------------|---------------------|---------------------------|---------------------------|-----------------------------|---------------------------------|
| 2.00 PREPARING | COMPTAGE | | | | | | | | | |
| 3.00 STRESS RE | 650 +/- 25°F | 2 hrs | air | | | 701 | | | | |
| 4.00 FINAL INSP | | | | | | | 12-05-2012 | | | 12-05-2012 |

COMMENTAIRES / comments

LES TRAITEMENTS THERMIQUES SUR CETTE COMMANDE A ÉTÉ FAIT EN UTILISANT DES ÉQUIPEMENTS EN CONFORMITÉ AVEC LES REQUIS DE LA SPÉCIFICATION AMS2759. TOUTES LES OPÉRATIONS DE TRAITEMENT THERMIQUE ONT ÉTÉ FAITES EN CONFORMITÉ AVEC LES REQUIS DE LA SPÉCIFICATION DEMANDÉE ET TOUTES LES VÉRIFICATIONS ET LES TESTS DEMANDÉES ONT ÉTÉ FAITES ET DOCUMENTÉES.

AUCUN CHANGEMENT OU DÉROGATION N'A ÉTÉ FAITE PAR RAPPORT AU TRAITEMENT THERMIQUE DEMANDÉ. ON CERTIFIE QUE LE MATÉRIEL A ÉTÉ FABRIQUÉ, ÉCHANTILLONNÉ, TESTÉ ET INSPECTÉ EN ACCORD AVEC LES SPÉCIFICATIONS DU MATÉRIEL ET LE BON DE COMMANDE ET LE MATÉRIEL RENCONTRE LES EXIGENCES SPÉCIFIÉS.

ACCOMPLISHED USING HEAT TREATMENT EQUIPMENT THAT MEETS THE REQUIREMENTS OF AMS 2759. ALL THE HEAT TREATMENT OPERATIONS WERE ACCOMPLISHED IN ACCORDANCE WITH THE REQUESTED/REQUIRED HEAT TREATMENT SPECIFICATION AND ALL REQUIRED VERIFICATIONS TEST HAVE BEEN PERFORMED AND DOCUMENTED. NO UNAUTHORIZED CHANGES OR ALL THE HEAT TREATMENT PROCESSING PERFORMED ON THIS ORDER WAS DEVIATIONS TO REQUIRED HEAT TREATMENT SPECIFICATIONS OR PROCEDURES HAVE BEEN PERFORMED.

WE CERTIFY THAT THE MATERIAL WAS MANUFACTURED, SAMPLED, TESTED AND INSPECTED IN ACCORDANCE WITH THE MATERIAL SPECIFICATION AND THE PURCHASE ORDER AND WAS FOUND TO MEET THE REQUIREMENTS.

APPROUVÉ par / Approved by:

Isabel Den



DATE: 2012-12-05

/ Nous certifions que toute l'information comprise sur ce rapport est exacte et conforme aux requis du client. / We certify that all the information on this report is exact and in accordance with the order requirements.

METCOR INC.

560 BOUL. ARTHUR-SAUVÉ
ST-EUSTACHE, QC, J7R 5A8

Tel: 450-473-1884 / Fax: 450-491-5498

Certificat de Conformité Détaillé

Detailed Certificate of Compliance

| BON DE TRAVAIL order | CHARGEMENT load |
|-------------------------|--------------------|
| 181760 | 1 |

CLIENT / customer 215

DART AEROSPACE
1270 ABERDEEN
HAWKESBURY

ON K6A 1K7

LIVRÉ À / shipped to:

DART AEROSPACE
1270 ABERDEEN
HAWKESBURY

ON K6A 1K7

1

| COMMANDE DU CLIENT customer po | BON DE LIVRAISON DU CLIENT customer shipper no. | MATÉRIEL material | CODE DE TRAITEMENT mat'l heat code | NUMÉRO DE LOT lot number |
|-----------------------------------|--|----------------------|---------------------------------------|-----------------------------|
| PO18563 | | Steel | | |

SPÉCIFICATIONS DU PROCÉDÉ processing specifications

STRESS REL

SAE AMS 2759/1 REV.E

| EXIGENCE / requirement | SPÉCIFICATIONS / specified | TESTS EXÉCUTÉS / performed | RÉSULTATS DE TESTS / results |
|------------------------|----------------------------|----------------------------|------------------------------|
| Visual | | | |

| QUANTITÉ quantity | POIDS weight | DESCRIPTION DES PIÈCES parts description |
|----------------------|-----------------|--|
| 5 | 150 | D350-748-101 (1) CROSSTUBE REFERENCE: 93257 (1) D350-748-101 CROSSTUBE REFERENCE: 85565 (1) D350-748-201 CROSSTUBE REFERENCE 92143 (1) D3350-748-201 CROSSTUBE REFERENCE: 89992 (1) D350-748-201 CROSSTUBE REFERENCE 93739 CONTENANT: 1 NIL |

| Operation | Temp. spécifiée Specified Temp | Temps de trempage Spécifié Specified Soak Temp | Atmosphère | Carbone Carbon Potential | Q-Media Q-Temp | Four # Furnace # | Date Départ Start Date | Heure d'entrée Time In | Heure de sortie Time Out | Date Complétée Date complete |
|---------------------|-----------------------------------|---|------------------|--------------------------------|-------------------|---------------------|---------------------------|---------------------------|-----------------------------|---------------------------------|
| 1.00 CONT. INIT. | LAVAGE | | si nécessaire | | | | | | | |



Metcor Inc.

560, boul. Arthur-Sauvé, St-Eustache (Québec) J7R 5A8

Tél. 450 473-1884

Télécopieur/Fax administration 450 491-5498

Télécopieur/Fax production 450 491-6454

Page 1 / 2

Certificat de Conformité
Certificate of Compliance

| BON DE TRAVAIL order | CHARGEMENT load |
|-------------------------|--------------------|
| 181760 | 1 |

CLIENT / customer 215

DART AEROSPACE

1270 ABERDEEN

HAWKESBURY

ON K8A 1K7

LIVRÉ À / shipped to:

DART AEROSPACE

1270 ABERDEEN

HAWKESBURY


ON K8A 1K7

1

CERTIFIÉ par / Certified by:



DATE: 2012-12-05

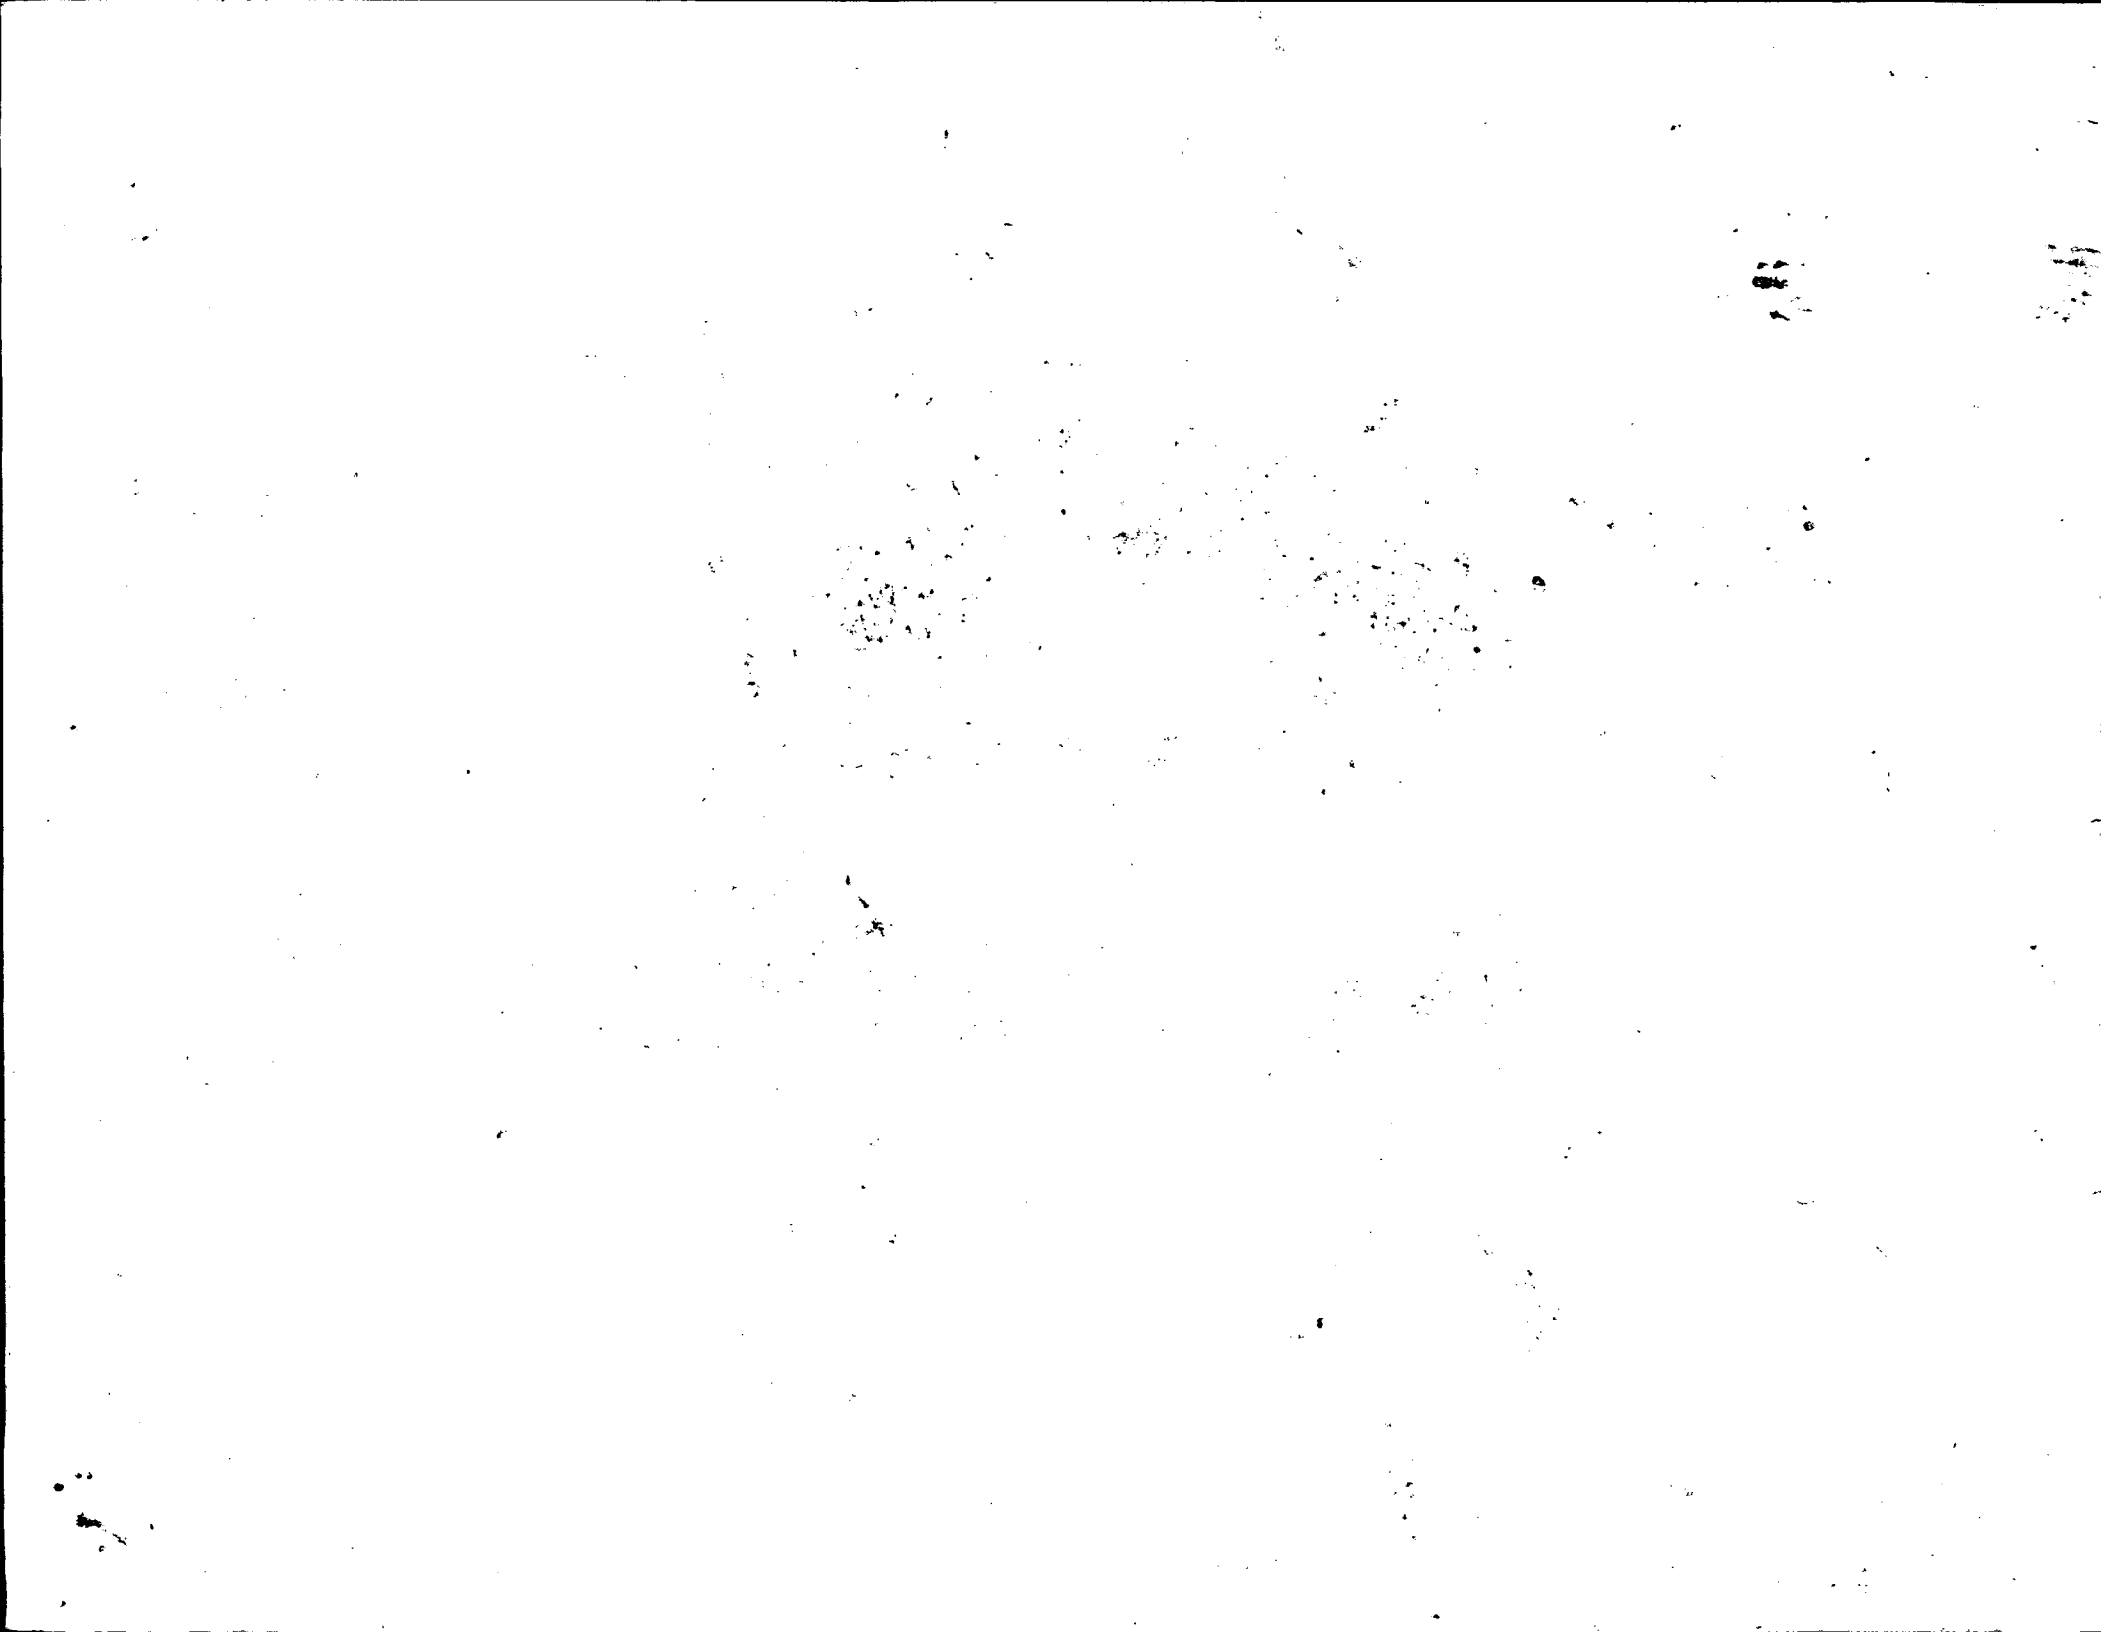

**CERTIFICATE OF
CONFORMANCE**

**CADORATH PLATING CO. LTD.
2150 LOGAN AVENUE
WINNIPEG, MANITOBA R2J-0J1**

DATE: Dec-18-2012

CONIGNED TO: Dart Aerospace Ltd.
1270 Aberdeen St.
Hawksbury, ON K6A 1K7

W/O #: 120133
INVOICE #: 63813

**CONTRACT OR
PURCHASE ORDER #** 18601

DESCRIPTION: CROSSTUBE

QTY 1

P/N # D350-748-201

S/N # B93738

CADMIUM PLATING IAW AMS-QQ-P-416C TYPE 2 YELLOW CLASS 1.
MPI IAW ASTM-E-1444. BAKE HEAT CHART # 12-1298 AND # 12-1316.

CERTIFICATE: I certify that the items indicated here on have
been inspected and tested and conform to all specifications
and requirements detailed on the contract or purchase order.



Approved Inspector: _____

A handwritten signature in black ink, appearing to be 'R. J. ...', written over a horizontal line.



LIQUID PENETRANT TEST REPORT

P- 12689

PAGE 1 OF 1

CLIENT DART AEROSPACE DATE DEC-20-12 TIME AM ☒ PM ☐
ATTENTION CHANTEL LOVIE ACUREN JOB NO. 108-12-0928
ADDRESS 1270 ABERDEEN ST. POWO No. ---
HAWKES BURY WORK LOCATION SAME
ACCEPTANCE STD. ASTM 1417/25F038 REV./DATE 2005
PROJECT F.P.I. ON CROSS TUBES AND MACHINED PARTS
ITEM(S) EXAMINED 9 - CROSS TUBES
8 - MACHINED PARTS (SLEEVES)

JOB DESCRIPTION --- PROCEDURE NO. LT-002 REV./DATE 2008 TECHNIQUE NO. LT-002 REV./DATE 2008
PART NO. SEE RESULTS MATERIAL STEEL/Aluminum THICKNESS VARIOUS
SCOPE A WET FLUORESCENT DYE INSPECTION WAS CARRIED OUT ON
THE SURFACE ONLY 100%

TEST DETAILS

| | | | | | |
|-------------------|---|----------------------------------|--|--|--|
| METHOD | <input checked="" type="checkbox"/> FLUORESCENT | <input type="checkbox"/> VISIBLE | <input checked="" type="checkbox"/> WATER WASH | <input type="checkbox"/> SOLVENT REMOVABLE | <input type="checkbox"/> POST EMULSIFIED |
| FAMILY BRAND | <u>MAGNA FLUX</u> | | BLACK LIGHT S/N | <u>16459</u> | <input type="checkbox"/> OUTPUT > 1000 μ W/cm ² |
| PENETRANT | <u>2LG2</u> | MINIMUM DWELL TIME | <u>45</u> | MIN. | <input type="checkbox"/> AMBIENT < 2 fc |
| PENETRANT REMOVER | <u>H2O</u> | MINIMUM DRY TIME | <u>>10</u> | MIN. | LIGHTING EQUIP. <input type="checkbox"/> FLASHLIGHT <input type="checkbox"/> TROUBLELIGHT <input type="checkbox"/> OUTPUT > 100 fc @ SURFACE |
| DEVELOPER | <u>SKD52</u> | MINIMUM DWELL TIME | <u>10</u> | MIN. | OTHER <u>LABINO</u> |
| DEVELOPER TYPE | <input checked="" type="checkbox"/> NON AQUEOUS | <input type="checkbox"/> AQUEOUS | <input type="checkbox"/> DRY | LIGHT METER S/N | <u>1098866</u> |
| | | | | CAL DUE DATE | <u>JULY-2013</u> |

TEST SURFACE

| | | | | | |
|---------------------|--------------------------------------|---|---|---------------------------------------|--|
| SURFACE CONDITION | <input type="checkbox"/> AS GROUND | <input type="checkbox"/> AS WELDED | <input checked="" type="checkbox"/> MACHINED | <input type="checkbox"/> SHOT BLASTED | <input checked="" type="checkbox"/> CLEAN BARE METAL |
| SURFACE TEMPERATURE | <input type="checkbox"/> < -4°C/20°F | <input type="checkbox"/> -4°C/20°F TO 10°C/50°F | <input checked="" type="checkbox"/> 10°C/50°F TO 52°C/125°F | <input type="checkbox"/> > 52°C/125°F | |

RESULTS- (☐ METRIC ☐ IMPERIAL)

| ITEM | COMMENTS | ACCEPT | REJECT |
|------|------------------------|--------|--------|
| 8 | SLEEVE'S - W.O.# 88239 | ✓ | |
| | CROSSTUBE - W.O.# | | |
| 1 | 92143 | | |
| 1 | " " 93738 | ✓ | |
| 1 | " " 94301 | ✓ | |
| 1 | " " 94300 | ✓ | |
| 1 | " " 94409 | | x |
| 1 | " " 94424 | ✓ | |
| 1 | " " 94427 | ✓ | |
| 1 | " " 94425 | ✓ | |
| 1 | " " 94426 | ✓ | |

SMS 12-1300

INDICATIONS

Scope of Services

The agreement of Acuren Group Inc. to perform services extends only to those services provided for in writing. Under no circumstances shall such services extend beyond the performance of the requested services. It is expressly understood that all descriptions, comments and expressions of opinion reflect the opinions or observations of Acuren Group Inc. based on information and assumptions supplied by the owner/operator and are not intended nor can they be construed as representations or warranties. Acuren Group Inc. is not assuming any responsibilities of the owner/operator and the owner/operator retains complete responsibility for the engineering, manufacture, repair and use decisions as a result of data or other information provided by Acuren Group Inc. In no event shall Acuren Group Inc.'s liability in respect of the services referred to herein exceed the amount paid for such services.

Standard of Care

In performing the services provided, Acuren Group Inc. uses the degree, care and skill ordinarily exercised under similar circumstances by others performing such services in the same or similar locality. No other warranty, expressed or implied, is made or intended by Acuren Group Inc.

SIGNATURES

| | | | | | | |
|-------------------------|----------------------|----------------------------|----------------|----------------------------|----------------------|----------|
| CLIENT REPRESENTATIVE | <u>Andy Sheldon</u> | PRINT | <u>Sheldon</u> | SIGNATURE | DTR # <u>E120263</u> | |
| TECHNICIAN (SIGNATURE): | <u>Mike Johnston</u> | 1 ST TECHNICIAN | | 2 ND TECHNICIAN | REPORT REVIEWED BY: | |
| NAME (PRINT): | <u>Mike Johnston</u> | CGSB LEVEL <u>II</u> | SNT LEVEL | CGSB LEVEL | NAME | INITIALS |
| | | CGSB REG. No <u>106016</u> | | CGSB REG. No | | |

5.0 PARTS LIST

| Qty -101 | Qty -201 | Part Number | Description |
|-------------|-------------|---------------|---|
| X | | D350-748-101 | CROSSTUBE INSTALLATION, AS 350/355 HIGH FWD |
| | X | D350-748-201 | CROSSTUBE INSTALLATION, AS 350/355 HIGH AFT |
| 1 | | D350-748-141 | CROSSTUBE ASSEMBLY, AS 350/355 HIGH FWD |
| | 1 | D350-748-241 | CROSSTUBE ASSEMBLY, AS 350/355 HIGH AFT |
| *2 | *2 | D3502-1 | SUPPORT |
| *2 | *2 | D2856-400-710 | ABRASION STRIP |
| *1 | *1 | AELS-1032-225 | INSERT |
| *2 | *2 | MS21920-20 | CLAMP |
| *1 | *1 | MS27039-1-10 | SCREW |
| *1 | *1 | AN960JD10 | WASHER |
| 4 | 4 | D350031 | SADDLE |
| 16 | 16 | D350151 | BUSHING |
| 16 | 16 | AN416A | BOLT |
| 8 | 8 | AN411A | BOLT |
| 4 | 4 | AN532A | BOLT |
| 32 | 32 | AN960JD416 | WASHER |
| 8 | 8 | AN960JD516 | WASHER |
| 24 | 24 | MS21042L4 | NUT (OR MS21042-4) |
| 4 | 4 | MS21042L5 | NUT (OR MS21042-5) |

* REFERENCE ONLY. PARTS ARE INCLUDED IN D350-748-141/241 ASSEMBLIES ABOVE

• COPYRIGHT © 2006 BY DART AEROSPACE LTD •

THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.

Revision: **B**

Date: 07.06.15
